

DCPP Project ID:

From: Cook County Department of Capital Planning & Policy

69 W Washington, Floor 30

Shannon E. Andrews, CPO

Office of Chief Procurement Officer

Chicago, IL 60602

23316

Date:02/21/2018

To:

Cook County, Purchasing 118 N. Clark Rm, 1018

Chicago, Illinois 60602

042132.00

Location:

Work Order Number:

2650 S California Ave

Chicago, IL 60608

Contract #:


1555-14475-MC5

Portfolio:

Public Safety

[,,,,,,,	The Residence of the Control of the	on seeded northware	The state of the s			
Contractor:	S Mechanical, Ir	ic.				
Work Order Title:	CCB Install Floo	r Drains-Penthouse & Equ	lipment Rooms	The AMerican Control of the American	The second secon	
					1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965 - 1965	
		se of Proposal Accept				
	If Revised:	Date:	min o 200 (20 No observation and propagation and propagation of the control of th		A CONTROL OF THE STATE OF THE S	
Your Work Order Propose	al has been acce	pted for the above Work a	s follows:		STANDARD CONTRACTOR OF THE STANDARD CONTRACTOR O	i
Work Order Amount:		\$354,618,16				
Licensing Fee for The Go (5.00% of Construction)	rdian Group	\$17,730.91			·	
Total Amount:		\$372,349.07				
MWBE Participation:	•	\$120,782.00	Section of the sectio	2 134 2 2 3 2 4 4 4 5 1 2 2 3 3		
Funding Source(s)	-	4 - Capital Renewal/De	eferred Maintenance			
Liquidated Damages		Liquidated Damages w	vill not apply			. 18
A notice to proceed will be	s issued which w	ill establish the Work Orde	er Start date and the com	pletion date.		
The CCOCPP JOC Coord	linator					
Requested By:	a)	2/17/18	When		7	/#1+
Shella Atkins, Project Cook County Depart Planning and Policy	tment of	Date	Eric Davis, Depu Gook County De Planning and Po	partment of		Date
Deamenh.	M Quy	2/28/18	No. of the second	B		n
Financial Arralyst		Date 3/4/18	Ann P. Kalayil, B (Signature requir		Over \$1 million)	Date
Earl Manning) Direct	*52	Date	Approved By:			
Cook County Depart Capital Planning & P			May 9		5 April 20	10

Date



Job Order Contract (JOC) Purchase Order Package Checklist

Job Order Number:	042132.00
Job Order Name:	CCB Install Floor Drains-Penthouse & Equipment Rooms
Job Order Location:	2650 S California Ave, Chicago ,IL 60608
Approved Proposal:	\$354,618.16
Contractor:	S Mechanical, Inc.
Construction Duration	: 4 Months
	Notice of Proposal Acceptance (NOPA) Cook County Board Approve Documentation If Applicable County Justification/Estimate (Provided by PM) Contractor Evaluation - Project Development Contractor's Job Order Proposal Package (See Below) Detailed Scope of Work with Project Duration (Signed by Contractor) Prawings (If applicable) Project Picture(s) Documenting Existing Conditions Detailed Construction Schedule (If Applicable)
	Approved Price Proposal Summary & Detail (Signed by Contractor) M/WBE Subcontractor Estimate, Disclosure of Retained Parties (Signed by Contractor) Utilization Plan (Signed by Contractor) For Each M/W/D/SBE Subcontractor:Letter of Intent (Signed by Subcontractor)/Current Certification Letter Identification of Sub-contractor/Sub-Consultant Form(ISF Form) COUPE Signatory Form & Backup Non Pre-Priced/Reimbursable Back Up (If Applicable) Special Insurance (If Applicable)
	Is Project Within Bond Capacity - Y/N
eviewed by Gordian A	AM/SAM: 2/23/18



TONI PRECKWINKLE

PRESIDENT

Cook County Board of Commissioners

RICHARD R. BÖYKIN

1st District

DENNIS DEER 2nd District

JERRY BUTLER

3rd District

STANLEY MOORE
4th District

DEBORAH SIMS 5th District

EDWARD M. MOODY 6th District

JESUS G. GARCIA 7th District

LUIS ARROYO, JR. 8th District

PETER N. SILVESTRI 9th District

BRIDGET GAINER 10th District

JOHN P. DALEY 11th District

JOHN A. FRITCHEY 12th District

LARRY SUFFREDIN

GREGG GOSLIN 14th District

TIMOTHY O. SCHNEIDER 15th District

JEFFREY R. TOBOLSKI 16th District

SEAN M. MORRISON 17th District DEPARTMENT OF CAPITAL PLANNING & POLICY

EARL MANNING

DIRECTOR

69 W. WASHINGTON, SUITE 3000 ◆ CHICAGO, ILLINOIS 60602 ◆ (312) 603-0312

February 27, 2018

TO:

Shannon E. Andrews, Chief Procurement Officer

Officer of the Chief Procurement Officer

FROM:

Sheila V. Atkins, Project Director

Department of Capital Planning and Policy

RE:

CCB Install Floor Drains- Penthouse and Equipment Rooms

Budget Justification - Work Order No. 042132.00

This memorandum serves as justification for procurement of construction services for the above project in the amount of \$354,618.16.

We find the pricing to be fair and reasonable. The price proposal has been compiled and reviewed by The Gordian Group, the Department of Capital Planning and Policy and the Department of Facilities Management (DFM), and PM STV/Heery.

Whenever water collects in either the equipment room or penthouse from the mechanical equipment there is no drainage system for the water except to go through the floor into the courtrooms, disrupting scheduled activities in these rooms, resulting in activities being cancelled or relocated.

The project scope is to provide a level coating of concrete, pitched towards new ejector pumps / drainage system, which are to be surrounded by curbs to assist in channeling the water for the east and west sides of the penthouse which is located above the courtrooms.

We respectfully request the approval and expediting of this package due to the construction season being underway.

Should you have additional questions please contact me at (312) 603-0336.



Job Order Number:

042132.00

Job Order Name:

CCB Install Floor Drains-Penthouse &

Equipment Rooms

Contractor: S Mechanical

Construction Start Date:

03/05/2018

Construction Amount; \$354,618.16

Contractor Evaluation - Project Procurement

1-3 proposals = 5 points 4 proposals = 4 points 5 proposals = 3 points 6 proposals = 2 points ≥ 7 proposals= 1 point

Construction Completion Date: 06/25/2018

S.No.	Description	Poors Average Excellent ⊗N/A
1	Rate the Contractor's availability to visit the Project Site with the Owner	1 2 3 A 5 X
2	Rate the quality of the Detailed Scope of Work	1 2 3 4 5 X
(3)	Yes or No, did the Contractor submit the first Price Proposal on time?	YES = 5 points
4	Rate the quality of the first Price Proposal	1 2 3 4 5 X
5	Rate the quality/timeliness of subsequent Price Proposals	1 2 3 X
6	Enter the number of Price Proposals submitted for this Project	4 = 4 points
0	Rate the quality of the Contractor's Final Package	1 2 3 A 5 X
8	Yes or No, did the contractor submit the Final Package on time?	YES = 5 points
9	Rate the quality of the Contractor's Construction Schedule	1 Z 3 4 5 X
10	Rate the quality of the Contractor's Communication and Responsiveness	1 2 3 F X
11	Rate the Contractor's overall performance during the Project Procurement Process	1 2 3 4 5 X
Poor=1.	Average=2 to 4 , 5 = Excellent, Yes = 5 Points, No = 1 Point	

Comments:

(Gordian to answer only questions 3, 6, & 8)



Cook County Department of Planning & Policy 69 W Washington Chicago, IL 60602

Job Order Contract

Cook County Department of Capital Planning & Policy

Contractor:

S Mechanical, Inc.

Work Order Number:

042132.00

Date: 21 February 2018

Work Order Title:

CCB Install Floor Drains-Penthouse & Equipment Rooms

considered part of this scope of work,

Provide a drainage system in the east and west sides of the Penthouse above the courtrooms. This shall be accomplished as follows: 1. Pour a new level of concrete over the existing floors on the east and west sides of the Penthouse, a. This new level shall provide gravity pitch to new sewage ejector systems that will ultimately remove the overflow. b. There shall be curbing and sloping provided to channel the water overflow towards a sewage ejector in each side of the Penthouse, c. Ali new concrete is to be water sealed, d. Only the floor areas where overflow is a problem will be addressed, 2. (1) Sewage ejector system will be added to the existing plumbing piping drainage system on each side of the Penthouse, a. Totaling two systems, 3. Electrical power work, 4.. Control of the ejectors will be stand alone utilizing a float switch, 5. Engineering work.

Brief Scope of Work:

Relevel floor to pitch towards the existing drains

Specific Submittals Required:

Sketches and Drawings:

Material Submittals:

Scheduling Requirements:

Price Proposal Due Date:

01/22/2018

Estimated Construction Start:

04/05/18

Estimated Construction Completion:

07/25/18

Special Conditions:

Liquidated Damages will not apply

Special Instructions:

Comments:

Estimated Project Duration:

*To be signed by Contractor if Final Scope of Work



HVAC Construction & Service

February 20, 2018

Ms. Sheila V. Atkins Project Director - Bureau of Asset Management Cook County - Capital Planning & Policy 69 W. Washington, Suite 3000 Chicago, Illinois 6060

RE: Engineering

CCB Install Floor Drains - Penthouse & Equipment Rooms Criminal Courts Building, 2600 S. California Avenue, Chicago, Illinois 60608 Work Order #042132.00

Dear Ms. Aikins,

We will provide the following concerning the engineering of the above referenced project:

We will employ a structural engineer to certify the added weight of the new concrete being poured on existing
penthouse floor will not jeopardize the integrity of the building.

a. S Mechanical will cover the cost of this engineer under our current proposed price.

2. We will provide design drawings identifying the locations where drainage is an issue.

a. The drawings will identify the locations of new concrete curbs and how the slope will be attained.

b. Control joints will be added where deemed necessary.

c. A detail for concrete finishing around the support legs of existing equipment will be on the drawings.

d. Locations of the sewage basins and sanitary tie-in's will be shown.

 We will certify that the concrete product selection and installation will produce a concrete floor slab that is free from cracks for long term use and that it is water sealed.

The condensate drain lines that are resting on top of the existing floor slab shall remain as is.

a. The drain lines must remain as is due to the requirement that a certain depth in the piping drop must be maintained to ensure malfunction does not happen to the equipment it serves.

The water sealed concrete will be poured around the existing drain lines.

This piping is not under pressure. Therefore, it should not leak.

- i. In the remote chance it does leak sometime in the future, then the concrete can be chipped out, the piping repaired and a small patch of concrete can be poured around the chipped out area to reseal the floor.
- We will provide submittals for approval for the sewage ejectors and their respective basins.
- 6. Electrical power and control will be provided ejectors.
 - a. Control will be by float switches in the basins.
 - b. Audible alarms for sump pumps.
 - c. Stand-alone controls.
- 7. We will provide dust and noise control.

The existing air-handling units will continue to function while we work on the floor.

a. These air-handling units draw air from two sources: Outside air and return air. Both sources of air are transmitted via enclosed ductwork. Therefore, air cannot enter the units from the penthouse space. This eliminates the need for filter changes in the air-handling units during our construction.

Permits will be obtained once we have a PO.

a. The cost will be reimbursed as a supplemental.

We trust the above meets with your approval. If you have any questions and/or comments, then please feel free to contact us.

Thank you,

Sincerely, S Mechanical, Inc.

David Amacher Sales Engineer / Project Manager



HVAC Construction & Service

February 2, 2018

Ms. Sheila V. Atkins
Project Director - Bureau of Asset Management
Cook County - Capital Planning & Policy
69 W. Washington
Suite 3000
Chicago, Illinois 6060

RE: Concrete Engineering

CCB Install Floor Drains - Penthouse & Equipment Rooms

Criminal Courts Building

2700 S. California Avenue, Chicago, Illinois 60608

Work Order #042132.00

Dear Ms. Atkins.

The following questions have been raised concerning the concrete work:

1. Will the weight of the new concrete pour be too great for the existing building structure to support?

2. How will slopes be established in the new concrete to allow for drainage to the new plumbing system?

The answers are as follows:

1. The total weight of the new concrete pour is less than 5% of the existing building structure. Standard practice for concrete structural design is that any added load that falls at or below this 5% will not have a negative effect of the on the performance of the existing structural system. Therefore, the added weight of the new concrete is not an issue concerning building structural safety.

2. The slopes of the new concrete pour will be established through the use of an underlayment substructure to establish said slopes. This system will be further described in the submittals that will

be forwarded for approval.

We trust the above meets with your approval. If you have any questions and/or comments, then please feel free to contact us.

Thank you.

Sincerely, S Mechanical, Inc.

David AmacherSales Engineer / Project Manager



HVAC Construction & Service

July 26, 2016

RE: Detailed Scope of Work
CCB Install Floor Drains-Penthouse & Equipment Rooms
Criminal Courts Building
2700 S. California Avenue, Chicago, Illinois 60608
Work Order #042132.00

Problem identification and requested solution:


- In the past, there has been an overflow of water in the Penthouse that has resulted in water running out over the courtroom ceilings and then drains into the courtrooms.
 - a. This overflow would damage the courtrooms and cause disruption of court proceedings.
 - b. This condition only exists in the east and west sides of the Penthouse.
 - i. These sides are north-south length wise.
 - c. The interconnecting east-west part of the Penthouse is not affected by this flooding. Therefore, work is not required in this part of the Penthouse.
- As an emergency stop gap measure, light weight angle Iron has been installed all around the perimeter of the Penthouse floor.
 - a. The angle iron is preventing the water flow to run out over the courtroom ceilings and then drain into the courtrooms.
 - b. This measure shall remain in place.
 - i. Alteration to this system is not required.
- 3. A solution to this problem is requested.


Solution (Scope of Work): Provide a drainage system in the east and west sides of the Penthouse above the courtrooms. This shall be accomplished as follows:


- 1. Pour a new level of concrete over the existing floors on the east and west sides of the Penthouse.
 - a. This new level shall provide gravity pitch to new sewage ejector systems that will ultimately remove the overflow.
 - b. There shall be curbing and sloping provided to channel the water overflow towards a sewage ejector in each side of the Penthouse.
 - c. All new concrete is to be water sealed.
 - d. Only the floor areas where overflow is a problem will be addressed.
- 2. (1) Sewage ejector system will be added to the existing plumbing piping drainage system on each side of the Penthouse.
 - a. Totaling two systems.
- 3. Electrical power work.
- 4. Control of the ejectors will be stand alone utilizing a float switch.
- Engineering work.


This proposal excludes the following:


- 1. Sales taxes.
- 2. BAS work.
- 3. Premium time labor rates.
- 4. Permits, fees or bonds.
 - a. These costs will be recouped under a supplemental purchase order,
- 5. Overtime and/or double-time labor rates except as noted above.

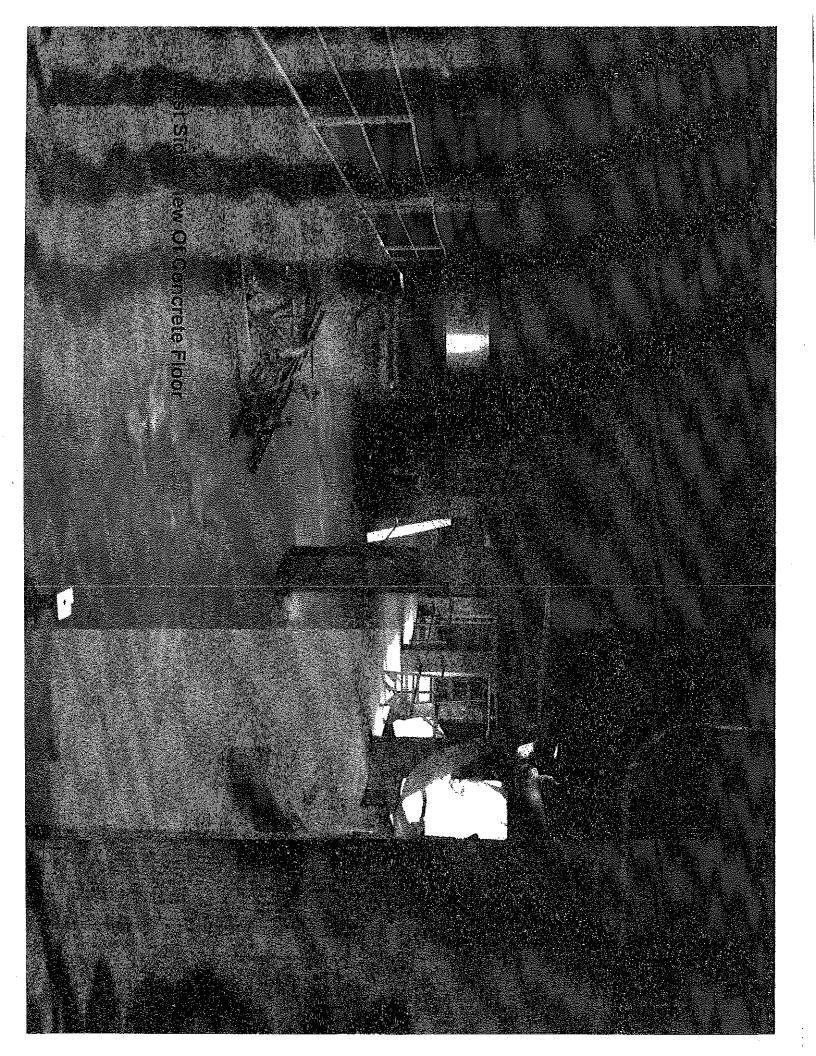


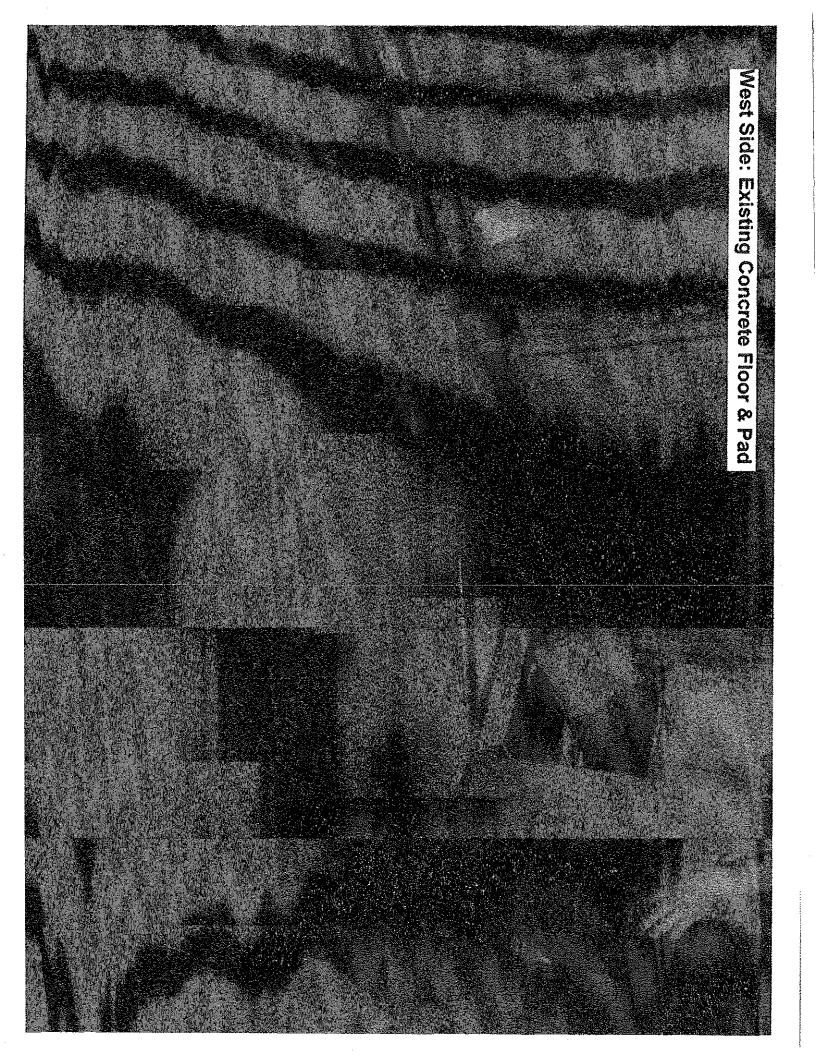


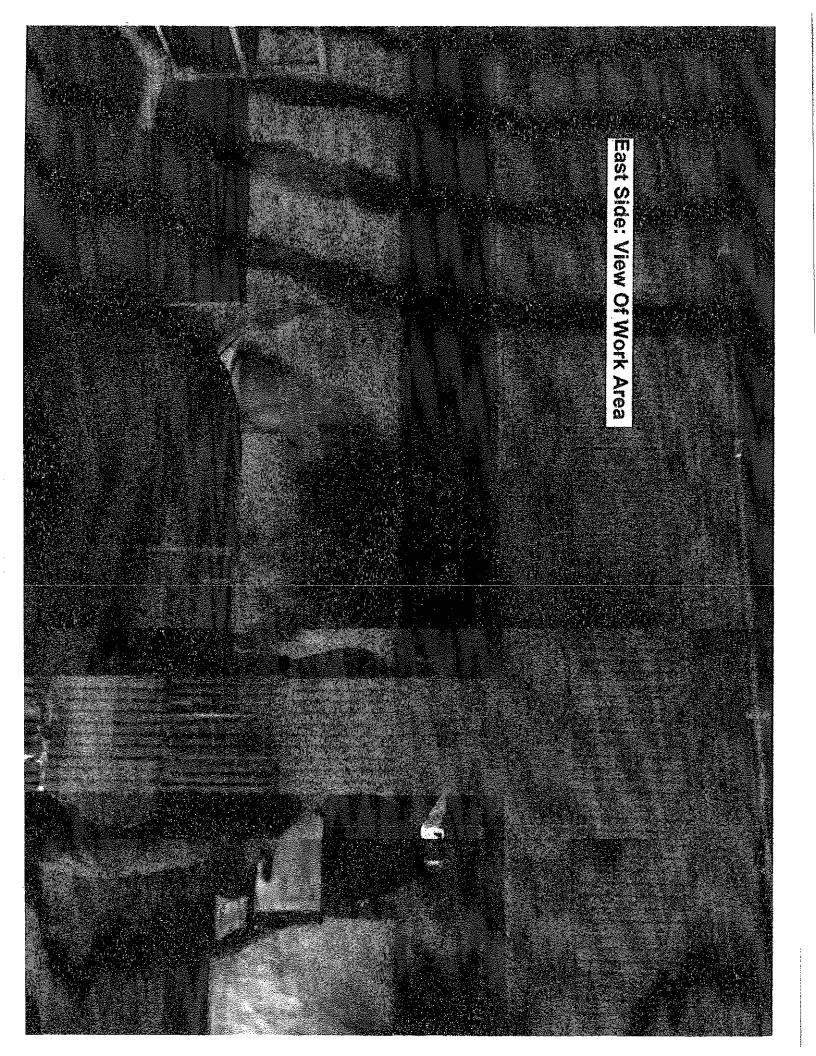

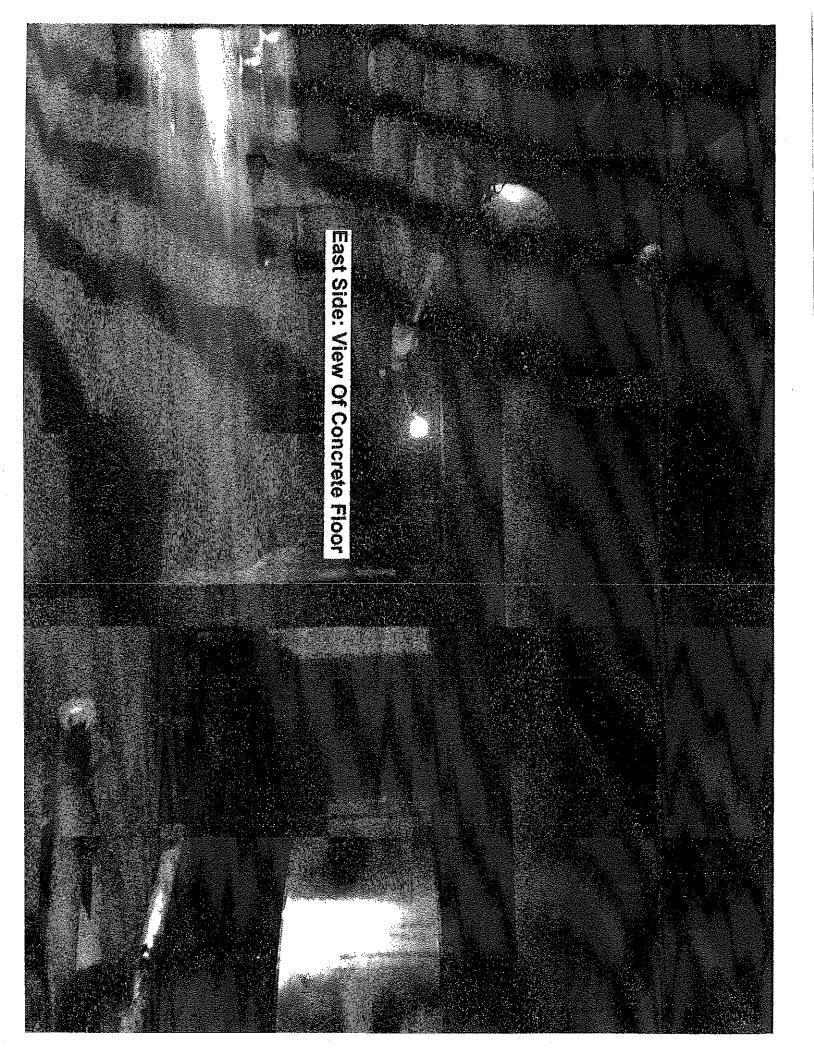

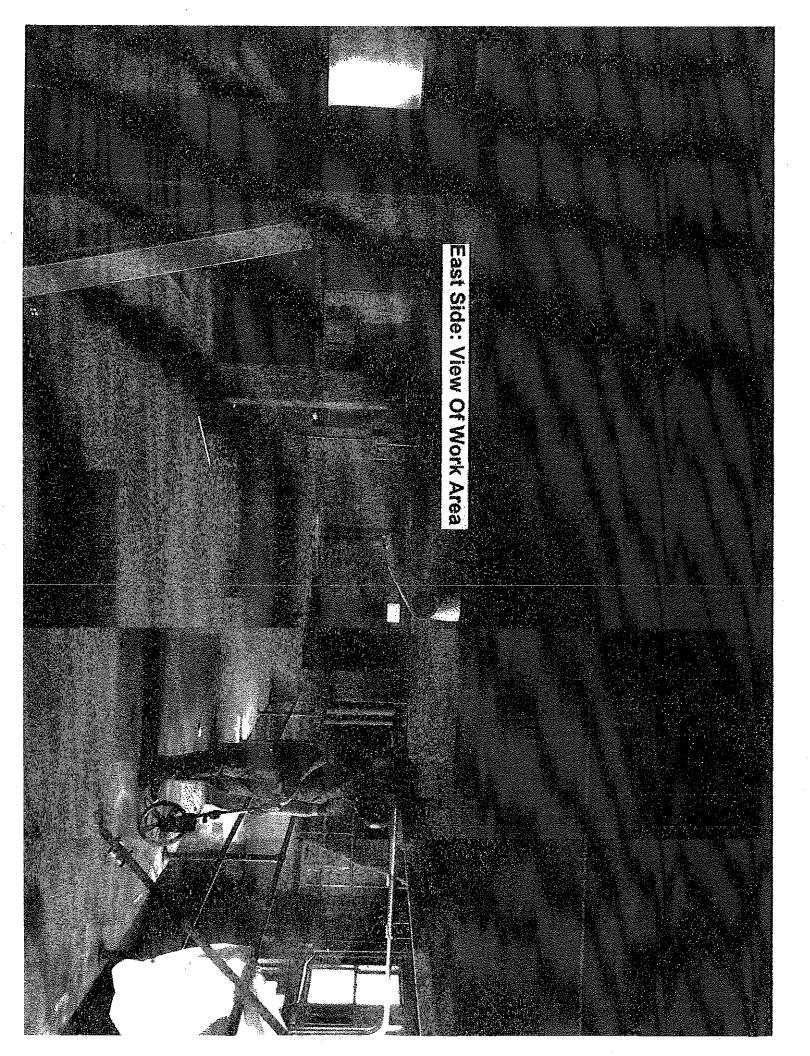

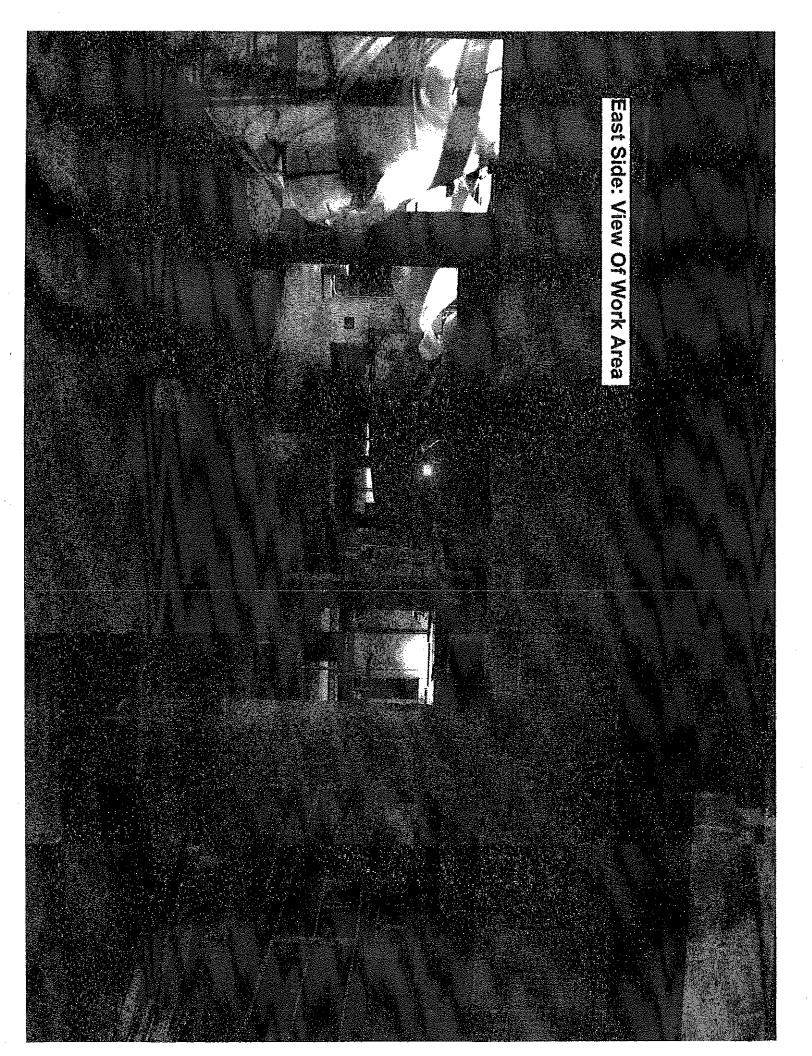

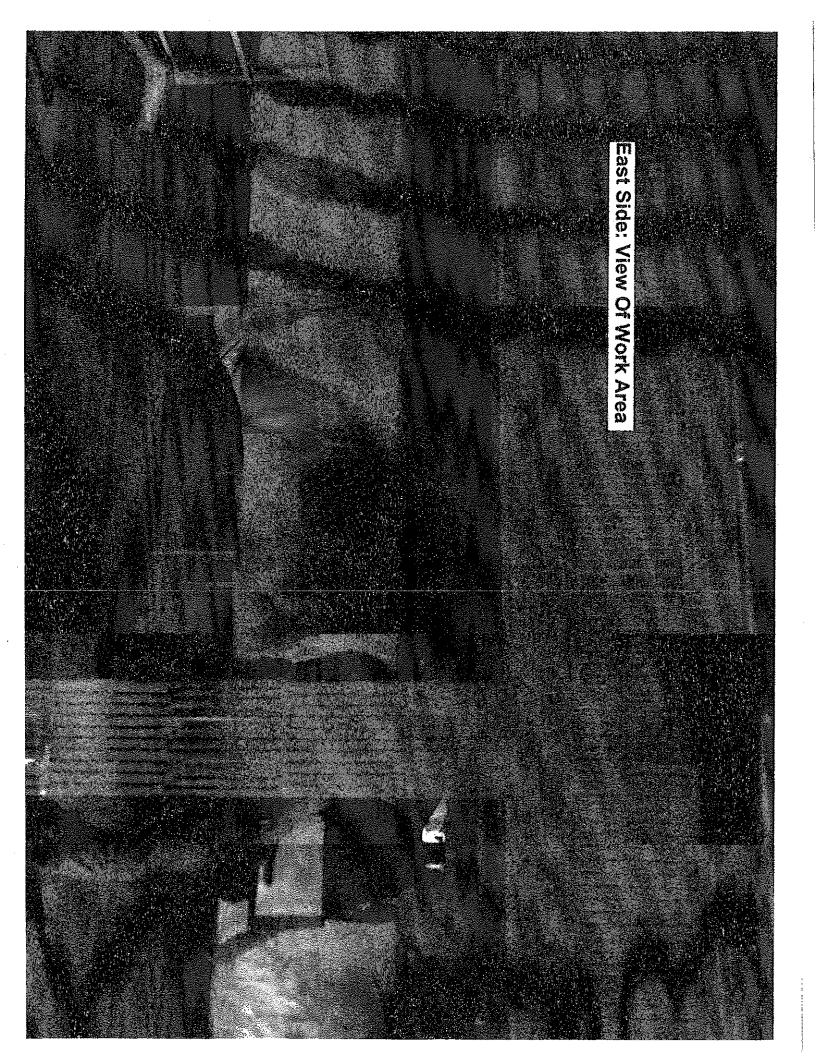

			Ī		•			Dake							
1	Activity ID	Activity (Withe		Electric Section	_		_					EO3			
20				-					Mar	Apr	May	ran)°	jaj,	Aug	Sap
10 March Controller Particle March Controller Partic	CCE Install FI	doi Dianis-Penthouse & Equipi	ment Rooms, W		: †			İ							
				-								••••			
Order Chein Conduction Family Chein Co	General					- 1	╗	30-War-18							****
Montabulic Mon	PHEC4020	ESDB NIP		4		- 1	05-Mar-18		♦ fesue N₹P						
Chain Contaction Family 1 1 1 1 1 1 1 1 1	PHEC-4030	MobBzation		-	,			304/var-18		Mobilization					
Stant Sunder Pumbig Plang Size Approve Sunger Planch Size Approve Size Approv	PAECHONO	Certain Construction Permit		-	- -	- 1	_	19-Mar-18	Obtain	Construction Permit					-
Status Rumbing Psych Status 10 10 10 10 10 10 10 10 10 10 10 10 10	Submittees			\dashv		- 1		16-Mate/18							
Status Savage Electro System SDA 10 0 07, 15 0 GAMEN 9 CHANGE 18 CHANG	SUB-1010	Submit Plumbing Ploing SDs		-	- [[-1	15-Mar-18	_	umbling Piping SDs					
Starting Starting Charled Starting Starting	SUB-1020	Submit Sawage Ejector System SDs		\dashv	٥		╗	16-Mar-18	_	Viriage Ejector System SDs					
Approve Plumbing Planing Size	SUB-1040	Submit Standard material SDs		-{	_	- 1	T	15-Mar-18		anderd material SDs					
Approve Plumbing Packs Approve Plumbing Packs Standard Maderials Approve Plumbing Packs	Herriew & Appr	cvals			 د			30-Mar-48		• • • •					
Approve Sewage Section Size in 10 10 0% 16 1944ar-18 So-Macra 8 Approve Sewage Excitor System Size 10 10 0% 26 1944ar-18 20-Macra 8 20-Macra	REV1000	Approve Plumbing Ploing SDs		-	_		г	30-Mar-₹8		Approve Plumbing Proing	SDs				
Approve Sandrat Materials State 10 10 0% 26 1944a-18 20-Mar-18 20-Mar-	REVIOU	Approve Sewage Ejector System SDs		_	-		⊏	30-Mar-18		Approve Sewage Ejector	System SDs				
Radio Pulmbing Pulmg Radio Pulmging Ra	REV-1030	Approve Standard Material SDs		-			Т	30-Mar-(8		Approve Standard Mater	tal SDs				
Rab Planching Pulm & Control Planching Pulm	Fabrication				g.			27- 40 r-18							
Fi2D Sewage Ejector System 20 20 20 0 0% 16 02Apr18 77 Apr16 Emission Planting Ejector System 10 10 0% 26 02Apr18 17-Apr16 Emission Planting Emissio	F&D-1000	F&D Plumbing Plping		Н	e e	ıı		27-Apr-18		9	&D Plumbing Ploing				-
R3.0 Standard Materials	750-1010	F&D Sewage Ejector System		-	9			27-Apr-18			&D Sewage Fjector Systel	 F			
Patal Punched Saves Ejectr Spanne (2)	FRD-1030	F&D Standard Materiels		_	0	1		13-Apr-18		Exercise P&D Standar	of Materials				
March Purchase Part Average & State Average Aver						-									
Firsted Purpling Paper & Somege Epocar Systemme (2)	A1040	Apply Concrete Roor Leveling & Seal		\dashv			<u>I</u>	17-14-18					Apply Cuty	and Roor Leveling &	- Tel-
Triang & Statup Triang & Statup	A1010	Install Plumbing Piping & Sewage Ejector	Systems (2)	4	١	i.	7	29-/un-18					trstall Plumbing Piping &	Sewage Ejedor Syster	18 (Z)
Site Reactives (Substantial Completion) Walk (Trough)	A1030	nstall Power & Controls		+				07-JUN-18				Install Power & Con			
Site Readiness (Substantial Completon) Walk Through		i resting ex examinp		-		Š	1.18-104-18	20~luk-18					Matter 10	A Start-up	•
Site Neutralists (Studential Completion) VMM (Timugh) 0 0 0 0 0 0 0 0 0															
Contract Compileton & Acceptance Contract Cont	0.5-1010	Site Reactness (Substantial Completion) \	Walk Through	1	_			16-10/-19*					是是 agg ◆	ress (Signetantial Con	pletton) Web The
Valuent Cassou Locumentation 1 0 % 2 33-Jul-18	0.5-1020	Complete Punch List Work		4	_	- !	19-04-18	24-441-18					1 1 1	photo Punch List Work	
Confeat Completion & Acceptance 0 0 0 0% 0 25-vit-18	2000	Subrat Cosecut Localmentation		- -	_	- 1	23-14-18	23-741-18					idus 1	A Gossaut Document	richt.
Contract Contract of the Contr	0.500	rital inspection		-	 	- 1	25-74-18	25-WH10						Jhypecton	•••
	acate of the	Comeac Completion & Acceptance		-		- 1	~	125-M-18					ψ Φ	fract Completion & Act	entence
	Fernalning Acust Wor	g Levelof Effort of	Project ID: WO#042232 Shart Date: 05-Mar-18	.0 Base00C			ł _				Date		www.TemulaceCco evision	Checked	Approved
Region Effort Project ID: WORK-64222.0 Basedoc San Date: CAle Parksin Chaban Parksin Chaban Chaban Parksin Chaban	EXEMPTE Formalning	g Work maining Work	Finish Date: 25-33/48 Data Onie: 05-Mar-18				_	S Mechanica Procession From	11, 13, 13, 13, 13, 13, 13, 13, 13, 13,	rafe i oi	22-Fab-18				
Fernal Integrated Ettors Project ID: WO 16492222 0. Base 00°C Start Date: 05-Mar-18 The bit Date: 25-Mar-18 The bit Date: 25-M											-				

Job Order Contract

APPROVED - Price Proposal Summary - CSI

Date:

February 21, 2018

Contract Number:

1555-14475-MC5

Job Order Number:

042132.00

Job Order Title:

CCB Install Floor Drains-Penthouse & Equipment Rooms

Contractor:

S Mechanical, Inc.

Proposal Value:

\$354,618.16

Proposal Name:

CCB Install Floor Drains-Penthouse & Equipment Rooms

01 - General Requirements:	\$61,098.41
02 - Existing Conditions:	\$2,621.24
03 - Concrete:	\$247,106.30
22 - Plumbing:	\$22,553.68
23 - Heating, Ventilating, And Air-Conditioning (HVAC);	\$2,489.49
26 - Electrical:	\$18,749.04
Proposal Total	\$354,618.16

This proposal total represents the correct total for the proposal. Any discrepancy between line totals, sub-totals and the proposal total is due to rounding of the line totals and sub-totals.

The Percent of NPP on this Proposal:

0.00%

Sheila Alkinis, Project Director

'Date

David Amacher, Sale Engineer / Project Manager

Data

Job Order Contract

APPROVED - Price Proposal Detail - CSI

February 21, 2018 Date: Contract Number: 1555-14475-MC5 Job Order Number: 042132.00 Job Order Title: CCB install Floor Drains-Penthouse & Equipment Rooms Contractor: S Mechanical, Inc. Proposal Value: \$354,618.16 CCB Install Floor Drains-Penthouse & Equipment Rooms Proposal Name: 0.8825-Normal Working Hours, 1.0000-No Adjustment Adjustment Factor(s) Used: C8I Number UOM Description Line Total 01 - General Requirements 01 22 16 00 0002 EΑ \$6,000,00 Reimbursable FeesReimbursable Fees will be paid to the contractor for eligible costs. The base cost of the Reimbursable Fee is \$1,00, insert the appropriate quantity to adjust the base cost to the actual Reimbursable Fee (e.g. quantity of 125 = \$125,00 Reimbursable Fee), if there are multiple Reimbursable Fees, list each one separately and add a comment in the "note" block to identify the Reimbursable Fee (e.g. sidewalk closure, road cut, verious permits, extended warrantee, expedited shipping costs, etc.), A copy of each receipt shall be submitted with the Price Proposal, Unit Price Total Quantity Factor Installation \$6,000.00 6,000.00 \$1_00 x 1:0000 User Note: Plumbing, concrete and power/control design, subcontractor direction, ensure conformance to the specifications, ongoing engineering input and punch list. The receipt will be submitted with our final package. Category1: Engineering Work 01 22 20 00 0008 HR \$4,525.85 Cement MasonFor tasks not included in the Construction Task Catalog® and as directed by owner only. Unit Price Total Quantity Factor \$4,525.85 Installation \$81.99 x 0.8625 = 64.00 User Note: Break out the existing concrete for two new floor drains and sanitary piping to approximately 8" below floor level. This work is for the two floor drains that are to be piped into the sewage basins. The work includes the concrete breakout for the basins. One basin is 4 SF of surface area that requires the concrete to be removed. Each basin has an additional 5 LF of piping to allow for the floor drain installation. The trench cut for this piping is 1 LF wide, All cuts are to be 8" deep into existing reinforced concrete. There are two basins. The cutting and removal of the reinforced concrete per basin requires (16) hours by a crew of two cement mesons. This equates to (32) hours per basin. Therefore, (2) Basins with piping x (32) Hours/basin ≈ (64) Hrs. Category1; Concrete Work 01 22 20 00 0008 HR \$33,660,99 Cement MasonFor tasks not included in the Construction Task Catalog® and as directed by owner only. Unit Price Quantity Factor Total Installation 478.00 581.99 0,0625 = \$33,660.99 User Note: Wash and sterilize floor by hand method. The concrete floor must receive a new layer of concrete and be sealed. To allow for this new layer, the floor must be washed and sterilized or the new layer will not adhere to the existing floor properly. The new concrete layer must adhere to the existing to prevent overflow seeping through the floor to the spaces below. There is 10,000 SF of floor area that requires this work. A crew is capable of washing and sterilizing 22 SF per hour. Therefore, 10,000 SF / 22 SF per hour = 476 Hours. Category1: Concrete Work

Job Order Number: 042132.00

Job Order Title:

Rec#	CSI	lumbi	r	Mod.	UOM	Description					Line Tot
01 - (Gener	al R	equirem	ents							
4	01 2	2 23	00 0880	·	DAY	1-1/2 Ton Capacity. Driver	8' To 10)' Bed, 4 x 2 Flat B	ed Truc	k With Full-Time Truck	\$14,082.
						Quantity		Unit Price		Factor	Total
					Installation	24,00	×	\$679,34	x	0,8625 =	\$14,062.34
Cat eg	ory1:	Ger	teral Con		project, One					and tools throughout the o t weeks of construction,Th	
5		13	00 0003		CY	Callect Existing Det	oris And	Load Into Truck O	r Dump	sterPer CY of debris	\$1,172.
					** **********	Quantity		Unit Price		Factor	Total
					Installation	80,0D	x	\$22,65	x	0,8625 =	\$1,172.14
ateg	ory1:	Gen	eral Con	User Note: ditions	Dally constr	action cleanup, One C	Y/day,				·
5	01 74	19	00 0014		EA					a delivery of dumpster, n-hezerdous material.	\$360,
						Quantity		Unit Price		Factor	Total
					Installation	1.00	x	\$418,53	x	0,8825 =	\$360.98
atego	oryt:	Gen	eral Conc		Required to	remove debris reaultir	ig from t	ne construction.			
7	01 91	13	00 0004		HR	Commissioning - H\	/AC/Med	hanical Systems			\$1,316.
						Quantity		Unit Price	*	Factor	Total
					Installation	8,00	x	\$190,74	×	0,8625 =	\$1,316,11
atego	ory1:	Plur	nbing Wo		Operational	checks after start up.	·				
				l Requiren	nents:						\$61,098.4
			ondition	3					·,		
8	02 41	19	13 0040		EA	Drill 8" Diameter Co	re in >4"	To 6" Concrete			\$1,300.0
						Quantity		Unit Price		Factor	Total
					Installation	8.00	x	\$188,41	×	0.8625 =	\$1,300.03
				User Note:	Cores throug	th walls to allow pipe t	o pass.				
			- lat								
atego	ory1:	Plun	nbing Wo	rk							
atego	02 41		13 0040	rk 0032	EA	For Horizontal Cores	, Add				
	<u> </u>				Partition out houses are a	Quentity	s, Add	Unit Price		Factor	Total
	<u> </u>				EA Installation		s, Add	Unit Price \$34,68		Factor 0.8625 =	
9	02 41	19		0032	Partition out houses are a	Quentity	a, Add		x		Total
9 atego	02 41 o ry1:	19 Pluta	13 0040	0032	Partition out houses are a	Quentity	×	\$34.68	x		Total \$239.29
9 atego	02 41 o ry1:	19 Pluta	13 0040 nbing W o	0032	Installation	Quentity 8,00	×	\$34.68	X		Total \$239.29
9 atego	02 41 o ry1:	19 Pluta	13 0040 nbing W o	0032	Installation	Quentity 8,00 Drill 4" Dlameter Con Quantity	x re in >10	\$34,68 "To 12" Concrete Unit Price	المستوالة خدم	0.8625 = Factor	Total \$239.29 \$922.3
atego	02 41 o ry1:	19 Pluta	13 0040 nbing W o	0032 zk	EA Installation	Quentity 6,00 Drill 4" Dlameter Con	x re in >10 x	\$34.65 "To 12" Concrete Unit Price \$133.68	المستوالة خدم	0.8625 =	\$239.29 \$922.3

Job Order Number: 042132.00

Job Order Title:

Rec#	CSI N	umber	Mod.	UOM	Description					Line Tot
02 -	Existi	g Condition	18							
11	02 41	19 13 0068	0032	EA	For Horizontal Core	s, Add				\$159.
					Quantity		Unit Price		Factor	Total
				nstallation	8.00	x	\$23,12	x	0.8625 =	\$159.53
ateg	jory1:	Power & Co Work	ntrol							
ubt	otal fo	r 02 - Existiı	ng Conditio	ns:						\$2,621.
)3 - (Concr	ete								
12	03 01	30 71 0005		SF	1/8" To 1/4", Epoxy	Cementi	ticus Morter Patci	n, Deck	And Floors	\$232,116,
					Quantity		Unit Price		Factor	Total
				Installation	16,000.00	×	\$16,82	×	0.8625 =	\$232,116,00
			User Note:	Apply water	proof membrane over	entire fit	oor area. This nev	v levet s	hall provide gravity pitch t	to new
									ere is 8,000 SF of ficor an	
				-	work per Penthouse.	There ar	e two Penthouses	s, There	fore, 8,000 SF x 2 Pentho	DUSES = 16,000
		A	1-	SF.						
ateg	ory1:	Concrete Wo	OPK							
13	03 11	13 00 0005		SF	Mat Foundation Woo	od Form	work			\$8,790.
		,			Quentity		Unit Price		Factor	Total
				Installation	1,140.00	×	\$8,94	х	0,8625 =	\$8,790.26
ateg	ory1:	Concrete Wo	ork	Curbing requ	uires 500 SF. Perimete	ır formwo	ork requires 160':	κ4' ≄6 _'	40 SF. Therefore, the lote	lis 1,140 SF.
14	03 11	13 00 0005	0003	SF	For Curved Formwor	k, Add				\$1,811.6
					Quantify		Unit Price		Factor	Total
				Installation	627,00	x	\$3.35	х	0.8825 =	\$1,811.64
ateg	ory1:	Concrete Wo	rk							
15	03 39	23 23 0005		CSF	2 Ply Reinforced, Co	ingrete (uring Waterproof	Paper		\$4,368,4
					Quantity		Unit Price		Factor	Total
				Installation	160,00	x	\$31.80	×	0,8625 =	\$4,388.40
			User Notes						mbrane over entire floor s	· •
					r from passing through		•			
atego	ory t:	Concrete Wo	rk	•						
ubto	tal for	03 - Concre	ate:							\$247,106.3
	lumbi					 	**************************************		,	\$241,100.
16		/// W/// /// // // // // // // // // //		. <u>-</u>	Alt min can		Daniel 200			
10	EZ U0	76 00 0006		EA	4" Floor Cleanout, Re Plug And Nickel Brot			t (ron) M	ith Cast Bronze Screw	\$695.1
					Quantity	THE COVE	unit Price	 ··	Factor	Total
				Installation	2,00	v	\$402.99	x	0,8625 =	\$695,16
			Hear Nate-		2,00 ut required by the plun	X objua co/		•-		ቀቡኋ4, [[
n4~~-	-maff -	Plumbing Wo		, ice, diadilo	ar radence by the binn	ming coo	er. Exiating to De	4011OR	al branks	
tego	21 y 1.	· · · · · · · · · · · · · · · · · · ·								

Job Order Number: 042132.00

Job Order Title:

Rec#				UOM	Description				<u></u>		Line Tota
22 - 1	Plumb	bing									
17	22 0	5 76 00 0040		EΑ	4" Cleanout Tee Wi	h Bronze	e Screw Plug And	Round	Polished Bronze (Cover	\$561,6
					Quantity		Unit Price		Factor		Total
				Installation	2.00	x	\$325.69	x	0.8825 =		\$561.64
		•	User Note:	Ficor cleano	ut required by the plu	mbing co	de.				
ateg	ory1:	Plumbing W	ork								
18	22 05	5 76 00 0070		EA	4" Threaded Brass I	Plug, Rai	sed Head				\$76.5
					Quantity		Unit Price	•	Factor		Total
				installation	2,00	x	\$48,13	x	0,8625 =		\$79.57
			User Note:	Required in	the vent stack after th	e aanitan	y piping, Existing t	be de	emolished,		
ateg	ory1:	Plumbing W	ork								
19	22 05	5 76 00 0070	0118	EΑ	For Plug Tapped Fo	r Center	Screw, Add				\$16,3
					Quentity		Unit Price		Factor		Total
				Installation	2,00	x	\$9.50	x	0,8625 =		\$16.39
ateg	ory1:	Plumbing W	ork								
20	22 13	3 16 00 0023		LF	4" Bell And Spigot C	ast Iron	Pipe				\$9,949.8
				,	Quantity		Unit Price		Factor		Total
				installation	400,00	×	\$28.84	x	0,8625 =		\$9,949,80
			Sat Hole.	floor. From e between the and sanitary basins, Each	s to be located at the leach basin, new sanita new basins and the event piping riser is 10 pipe consists of 100 lipe = 400 LF.	ry and si xisting pi 0 LF, The	anitary vent piping iping, The piping c are two sanita	shall b listance ry pipe:	e provided to allow from each basin to and two sanitary	v for the connec to an existing sa Vent pipes for b	tion nitary oth
		Plumbing W	ork	floor. From e between the and sanitery basins, Each 100 LF per p	ach basin, new sanita new basins and the e vent piping daer is 10 pipe consists of 100 lipe = 400 LF.	ry and se xisting pi 0 LF, The LF, There	anitary vent piping iping. The piping o ere are two sanita efore, (2) sanitary	shall b listance ry pipes pipes 1	e provided to allow from each basin to and two sanitary	v for the connec to an existing sa Vent pipes for b	tion nitary oth
Catego 21		Plumbing W		floor. From e between the and sanitary basins, Each	ach basin, new sanita new basins and the e vent piping riser is 10 pipe consists of 100	ry and se xisting pi 0 LF, The LF, There	anitary vent piping iping. The piping o ere are two sanita efore, (2) sanitary	shall b listance ry pipes pipes 1	e provided to allow from each basin to and two sanitary	v for the connec to an existing sa Vent pipes for b	tion nitary oth
			ork	floor. From e between the and sanitary basins. Each 100 LF per p	ach basin, new sanita new basins and the e vent piping daer is 10 pipe consists of 100 lipe = 400 LF.	ry and so xisting pi 0 LF, The LF, There	anitary vent piping iping. The piping o ere are two sanita efore, (2) sanitary	shall b listance ry pipes pipes 1	e provided to allow from each basin to and two sanitary	v for the connec to an existing sa Vent pipes for b	tition Initiary oth 8 x \$248.4 Total
21	22 13	16 00 0023	ork 0011	floor. From e between the and sanitery basins. Each 100 LF per p	ech basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 lipe = 400 LF.	ry and so xisting pi 0 LF, The LF, There	anitary verit piping oping. The piping of one are two earlitates afore, (2) senitary Pipe Installation,	shall b listance ry pipes pipes 1	e provided to allove from each basin to a and two sanitary (2) sanitary vent	v for the connec to an existing sa Vent pipes for b	ation Initary oth 8 x \$248.4
21	22 13		ork 0011	floor. From e between the and sanitary basins. Each 100 LF per p	ech basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 lipe = 400 LF. For Above Ground Countity	ry and so xisting pi 0 LF, The LF, There	anitary verit piping open are two earlitary ea	shall b listance ry pipes pipes 1	e provided to allove from each basin to a and two sanitary (2) sanitary vent p Factor	v for the connec to an existing sa Vent pipes for b	tition Initiary oth 8 x \$248.4 Total
21	22 13 ory1:	16 00 0023	ork 0011	floor. From e between the and sanitery basins. Each 100 LF per p	ech basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 lipe = 400 LF. For Above Ground Countity	ny and si xisting pi 0 LF, The LF. There Cast Iron	anitary verit piping of the piping of the piping of the series are two sanitary effore, (2) sanitary Pipe Installation, Unit Price \$0.72	shall b listance ry pipes pipes 1	e provided to allove from each basin to a and two sanitary (2) sanitary vent p Factor	v for the connec to an existing sa Vent pipes for b	tition Initiary oth 8 x \$248.4 Total
21	22 13 ory1:	16 00 0023	ork 0011	floor. From e between the and sanitery basins. Each 100 LF per p LF Installation	ech basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 ipe = 400 LF. For Above Ground C Quantity 400.00	ny and si xisting pi 0 LF, The LF. There Cast Iron	anitary verit piping of the piping of the piping of the series are two sanitary effore, (2) sanitary Pipe Installation, Unit Price \$0.72	shall b listance ry pipes pipes 1	e provided to allove from each basin to a and two sanitary (2) sanitary vent p Factor	v for the connec to an existing sa Vent pipes for b	tion Initary oth s x \$248.4 Total \$248.40
21	22 13 ory1:	16 00 0023	ork 0011 ork	floor. From e between the and senitery basins. Each 100 LF per p	ech basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400,00 4" Bell And Spigot C Quantity 4,00	ry and sexisting pi 0 LF, There LF, There cast iron	anitary verit piping of the pi	shall b listance ry pipes pipes 1	e provided to allove from each basin to a and two sanitary (2) sanitary vent p Factor 0.8625	v for the connec to an existing sa Vent pipes for b	tion initary oth 8 x \$248.4 Total \$248.40
21 atego	22 13 ory1: 22 13	16 00 0023 Plumbing W	ork 0011 ork User Note:	floor. From e between the and senitery basins. Each 100 LF per p	ach basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400.00 4" Bell And Spigot C Quantity	ry and sexisting pi 0 LF, There LF, There cast iron	anitary verit piping of the pi	shall bistance ry pipes pipes d	e provided to allove from each basin to a and two sanitary P (2) sanitary vent p Factor 0.8625	v for the connec to an existing sa Vent pipes for b	tion initary oth 8 x \$248.4 Total \$248.40 \$523.8
21 atego	22 13 ory1: 22 13	16 00 0023	ork 0011 ork User Note:	floor. From e between the and senitery basins. Each 100 LF per p	ech basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400,00 4" Bell And Spigot C Quantity 4,00	ry and sexisting pi 0 LF, There LF, There cast iron	anitary verit piping of the pi	shall bistance ry pipes pipes d	e provided to allove from each basin to a and two sanitary P (2) sanitary vent p Factor 0.8625	v for the connec to an existing sa Vent pipes for b	tion initary oth 8 x \$248.4 Total \$248.40 \$523.8
21 atego	22 13 ory1: 22 13	16 00 0023 Plumbing W	ork 0011 ork User Note:	floor. From e between the and senitery basins. Each 100 LF per p	ech basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400,00 4" Bell And Spigot C Quantity 4,00	ny and sexisting pi O LF, There LF, There Cast Iron x ast Iron I	anitary verit piping of the pi	shall bistance ry pipes pipes -	e provided to allove from each basin to a and two sanitary P (2) sanitary vent p Factor 0.8625	v for the connec to an existing sa Vent pipes for b	tion initary oth 8 x \$248.4 Total \$248.40 \$523.8
21 Satego 22	22 13 ory1: 22 13	Plumbing W 16 00 8034	ork 0011 ork User Note: ork	floor. From e between the and sanitery basins. Each 100 LF per p LF Installation EA Installation Long sweep	ech basin, new senita new basins and the e vent piping daer is 10 pipe consists of 100 lipe = 400 LF. For Above Ground C Quantity 400.00 4" Bell And Spigot C Quantity 4,00 el is required to run pi	ny and sexisting pi O LF, There LF, There Cast Iron x ast Iron I	anitary verit piping of the pi	shall bistance ry pipes pipes -	e provided to allove from each basin to a and two sanitary P (2) sanitary vent p Factor 0.8625	v for the connec to an existing sa Vent pipes for b	tion Initary oth s x \$248.4 Total \$248.40 \$523.8 Total \$523.81
21 22 22 atego	22 13 22 13 22 13 22 13	Plumbing W 16 00 0034 Plumbing W 16 00 0034	ork 0011 ork User Note: ork	floor. From e between the and sanitery basins. Each 100 LF per p LF Installation EA Installation Long sweep	ach basin, new senita new basins and the e vent piping daer is 100 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400.00 4" Bell And Spigot C Quantity 4,00 el is required to run pi	ny and sexisting pi O LF, There LF, There Cast Iron x ast Iron I	anitary verit piping of ping. The piping of the piping of the piping of the piping of the pipe installation, Unit Price \$0.72 Long Sweep Unit Price \$151.83 ew location,	shall billistance ry pipes pipes 4 Add	Factor 0.8625 =	v for the connec to an existing sa Vent pipes for b	stion initary oth 8 x \$248.4 Total \$248.40 \$523.8 Total \$523.81
21 22 22 atego	22 13 22 13 22 13 22 13	Plumbing W 16 00 8034	ork 0011 ork User Note: ork	floor. From e between the and senitery basins. Each 100 LF per plus LF installation EA installation Long sweep	ach basin, new senita new basins and the e vent piping deer is 100 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400,00 4" Bell And Spigot C Quantity 4,00 el la required to run pi For Above Ground C Quantity	existing pion of the control of the	anitary verit piping open are two earlitary earlitary. The piping of earlitary earlitary. Pipe Installation, Unit Price \$0.72 Long Sweep Unit Price \$151.83 ew location, Pipe Installation, Unit Price	shall billistance ry pipes pipes 4 Add	Factor 0.8625 = Factor 0.8625 =	v for the connec to an existing sa Vent pipes for b	stion initary ofth 8 x \$248.4 Total \$523.81
21 22 22 23 atego	22 13 22 13 22 13 22 13	Plumbing W 16 00 0034 Plumbing W 16 00 0034	ork 0011 ork User Note: ork	floor. From e between the and senitery basins. Each 100 LF per plus LF installation EA installation Long sweep	ach basin, new senita new basins and the e vent piping deer is 100 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400,00 4" Bell And Spigot C Quantity 4,00 el la required to run pi For Above Ground C Quantity	ry and sexisting pi 0 LF, There LF, There Cast Iron x ping to n cast Iron x	anitary verit piping of the piping. The piping of the pipi	shall billistance ry pipes pipes 4 Add	Factor 0.8625 = Factor 0.8625 =	v for the connec to an existing sa Vent pipes for b	stion initary ofth 8 x \$248.4 Total \$523.81
21 22 22 23 atego	22 13 22 13 22 13 22 13	Plumbing Works 16 00 0034 Plumbing Works 16 00 0034 Plumbing Works 16 00 0034	ork 0011 ork User Note: ork	floor. From e between the and sanitary basins. Each 100 LF per p LF Installation EA Installation EA Installation	ach basin, new sanita new basins and the e vent piping daer is 10 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 4,00 el is required to run pi For Above Ground C Quantity 4,00 Quantity 4,00	ry and sexisting pi 0 LF, There LF, There Cast Iron x ping to n cast Iron x	anitary verit piping of the piping. The piping of the pipi	shall billistance ry pipes pipes 4 Add	Factor 0.8625 = Factor 0.8625 =	v for the connec to an existing sa Vent pipes for b	stion initary of the second se
21 22 22 23 atego	22 13 22 13 22 13 22 13	Plumbing Works 16 00 0034 Plumbing Works 16 00 0034 Plumbing Works 16 00 0034	ork 0011 ork User Note: ork	floor. From e between the and sanitary basins. Each 100 LF per p LF Installation EA Installation EA Installation	ach basin, new senita new basins and the e vent piping daer is 100 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400.00 4" Bell And Spigot C Quantity 4,00 el is required to run pi For Above Ground C Quantity 4,00 4" Bell And Spigot C	ry and sexisting pi 0 LF, There LF, There Cast Iron x ping to n cast Iron x	anitary verit piping of the piping. The piping of the pipe installation, and the pipe installation and the pipe inst	shall billistance ry pipes ry pipes pipes 4 Add x x	Factor 0.8625 = Factor 0.8625 =	v for the connec to an existing sa Vent pipes for b	stion initary ofth a x \$248.4 Total \$248.40 \$523.81 Total \$9.76
22 22 Satego 23	22 13 22 13 22 13 22 13	Plumbing Works 16 00 0034 Plumbing Works 16 00 0034 Plumbing Works 16 00 0034	ork 0011 ork User Note: ork 0011	floor. From e between the and sanitery basins. Each 100 LF per p LF Installation EA Installation EA Installation EA Installation EA Installation	ach basin, new senita new basins and the e vent piping deer is 10 pipe consists of 100 pipe = 400 LF. For Above Ground C Quantity 400,00 4" Bell And Spigot C Quantity 4,00 el is required to run pi For Above Ground C Quantity 4,00 4" Bell And Spigot C Quantity 4,00 4" Bell And Spigot C Quantity 4,00 4" Bell And Spigot C Quantity	existing pion of the control of the	anitary verit piping oping. The piping of th	shall billistance ry pipes ry pipes pipes 4 Add x x	Factor 0.8625 = Factor 0.8625 = Factor	v for the connec to an existing sa Vent pipes for b	\$248.40 \$248.40 \$523.81 Total \$523.81 \$523.81

Job Order Number:

042132.00

Job Order Title:

Rec#	CSI N	umber	Mod.	MOU	Description						Line Total
22 - 1	Plumb	ing									
25	22 13	16 00 0052	0011	EA	For Above Ground	Cast Iro	n Pipe Installation, /	Add			\$17,46
					Quantity		Unit Price		Factor	•	Total
		-		Installation	00.8	x	\$2,53	×	0,8625	=-	\$17.46
Categ	огу1:	Plumbing Wo	ork		·						
26	22 13	18 00 0062		EA	4" Bell And Spigot (Cast iron	1 1/8 Bend				\$747.55
					Quantity		Unit Price		Factor		Total
		-		installation	8.00	×	\$108.34	x	0,8625	E	\$747.55
				1/8 Bend is	required to run piping	to new i	ocation.				
Categ	ory1:	Plumbing Wo	ork		· .						
27	22 13	18 00 0062	0011	. EA	For Above Ground	Cest Iro	n Pipe Installation, /	Add			\$19.53
				•	Quantity	•	Unit Price	•	Factor	•	Total
				Installation	8,00	· X	\$2,83	×	0.8625	=	\$19.53
Categ	ory1:	Plumbing Wo	ork								
28	22 13	16 00 0072		EA	4" Bell And Spigot (Cast (ror	ı Wya				\$510,98
					Quantity		Unit Price		Factor		Total
				Installation	4.00	x	\$148.11	x	0.8625	=	\$510.98
				Wye"s are n	equired to run piping t	o new lo	cation,				
Categ	ory1:	Plumbing Wo	ork	,							
29	22 13	16 00 0072	0011	БA	For Above Ground	Cast Iro	n Pipe Installation, A	Add			\$18.70
					Quantity		Unit Price		Factor		Total
				Installation	4.00	×	\$5,42	x	0,8625	=	\$18,70
Categ	огу1:	Plumbing Wo	rk								
30	22 13	16 00 0108		EA	4" Bell And Spigot C	ast Iron	i Combination VVye	And 1/	/8 Bend		\$538,16
					Quantity	•	Unit Price		Factor		Total
				Installation	4,00	ĸ	\$155,41	×	0,8625	- '	\$536.16
				Wye and 1/8	bend'"s are required	to run p	piping to new location	on.			
Catego	ory1:	Plumbing Wo	rk								
31	22 13	16 00 0106	0011	EA	For Above Ground (Cast Iro	s Pipe Installation, /	Add			\$18.70
					Quantity		Unit Price		Factor		Total
				Instalfation	4.00	×	\$5,42	x	0,8625	=	\$18,70
Catego	ory1:	Plumbing Wo	rk								
32	22 13	16 00 0158		EA	4" Bell And Spigot C	ast Iron	Sanitary Tee				\$325,56
					Quantity		Unit Price		Factor	***	Total
				Installation	2,00	x	\$188,73	x	0,8625	=	\$325.56
			User Note:	Required to	separate sanitary and	vent p	oing.				
Catego	ory1:	Plumbing Wo	rk								
33	22 13	18 00 0158	0011	EA	For Above Ground	Cast Iron	n Pipe Installation, /	Add			\$8,76
					Quantity		Unit Price		Factor		Total
				facetottedos	0.00				0.0006	=	\$8.75
				Installation	2,00	X	\$5.07	X	0,8625	_	φυ.τ.

Job Order Number: 042132.00

Job Order Title:

Rec#	CSI N	IGINDEI	Mod.	MOU	Description					Line Tot
22 -	Plumb	oing.							<u> </u>	
34	22 13	3 16 00 0213		EΑ	4" Bell And Spigot (ast Iron	n P-Trap			\$167.
					Quantity		Unit Price		Factor	Total
				installation	2,00	x	\$97,02	x	0,8625 =	\$167.36
			User Note:	Required to	trap sewage smells fr	om the	water discharge,			
ateg	ory1:	Plumbing W	lork.	•						
35	22 13	3 16 00 0213	0011	EA	For Above Ground (Cast Iro	n Pipe Installation,	Add		\$4.
					Quantity		Unit Price	***********	Fector	Total
				Installation	2,00	x	\$2.83	x	0.8625 =	\$4.88
ateg	ory1:	Plumbing W	ork							
36	22 13	19 13 0087		EA	12-5/8" Round Floor	Drain 1	With Sediment Buc	ket, 4" B	ottom Outlet, Satin Bronze	\$1,212,
					Top, Without Trap			-		***************************************
					Quantity		Unit Price		Factor	Total
				Installation	2,00	x	\$703,17	x	0,8625 ==	\$1,212.97
			User Note:	Required to	trap the water and dis	charge	Into the basin.			
ateg	ory1:	Plumbing W	ork							
37	22 13	29 13 0031		ĒΑ		Coate	d Floet, Add, Gener	ral Purpo	ose For vertical sewage	\$805.4
					pumps Quantity	. —	Liet Orien		Factor	W
				1-4-11-5			Unit Price		Factor	Total
							440004			
				Installation	2.00	×	\$486,91	х	0,8625 =	\$805.42
		Disconding Mi	User Note:		2.00 control pump.	x	\$466,91	х	0,8625 =	\$805,42
	<u> </u>	Plumbing W		Switches to		×	\$486,91	х	0,8625 =	\$805,42
ateg 38	<u> </u>	Plumbing W 29 16 0012			control pump. 1 HP Submersible S	ewage	Pump, 230 Volt, 3	Phase, S	3" To 4" Fianged	\$2,737.5
	<u> </u>			Switches to	control pump, 1 HP Submersible S Discharge, Epoxy-C	ewage	Ритр, 230 Volt, 3 ast Steel Housing.	Phase, S	3" To 4" Flanged øller	\$2,737.8
	<u> </u>			EA	ontrol pump. 1 HP Submersible S Diacharge, Epoxy-C Quantity	ewage oated C	Pump, 230 Volt, 3 cast Steel Housing Unit Price	Phase, S And Imp	3" To 4" Flanged eller Factor	\$2,737.s
	<u> </u>		ork	EA Installation	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00	ewage cated C	Pump, 230 Volt, 3 ast Steel Housing. Unit Price \$1,586,88	Phase, S And Imp	3" To 4" Flanged eller Factor 0.8625 ≃	\$2,737.8
38	.22 13	29 16 0012	ork User Note:	EA Installation	ontrol pump. 1 HP Submersible S Diacharge, Epoxy-C Quantity	ewage cated C	Pump, 230 Volt, 3 ast Steel Housing. Unit Price \$1,586,88	Phase, S And Imp	3" To 4" Flanged eller Factor 0.8625 ≃	\$2,737.s
38 ateg	.22 13	29 16 0012	ork User Note:	EA Installation Pump require	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00	ewage cated C	Pump, 230 Volt, 3 ast Steel Housing. Unit Price \$1,586,88	Phase, S And Imp	3" To 4" Flanged eller Factor 0.8625 ≃	\$2,737.s
38	.22 13	29 16 0012	ork User Note:	EA Installation	1 HP Submersible S Discharge, Epoxy-C Quantity 2.00 ed to discharge the wa	ewage oated C x ater from	Pump, 230 Volt, 3 Cast Steef Housing Unit Price \$1,586,88 In the floor to the se	Phase, S And Imp x wage sy	3" To 4" Flanged eller Factor 0.8625 = rstem.	\$2,737.s
38	.22 13	29 16 0012	ork User Note:	EA Installation Pump require	1 HP Submersible S Discharge, Epoxy-C Quantity 2.00 ed to discharge the was	x x ater from	Pump, 230 Volt, 3 Cast Steef Housing Unit Price \$1,586,88 In the floor to the se	Phase, S And Imp x wage sy	3" To 4" Flanged eller Factor 0.8625 = vstem,	\$2,737.3 Total \$2,737.39
38 ateg	.22 13	29 16 0012	ork User Note:	EA Installation Pump require	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the was Simplex Single Phas Submersible Sewag	x x ater from	Pump, 230 Volt, 3 cast Steef Housing. Unit Price \$1,586,88 In the floor to the se roller With NEMA 4	Phase, S And Imp x wage sy	t" To 4" Flanged eller Factor 0.8625 = vstem, sure For Non Autometic ng light, HOA switch, and	\$2,737.3 Total \$2,737.39 \$1,175.2
38	.22 13	29 16 0012	ork User Note:	EA Inatallation Pump requin	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the way Simplex Single Phase Submersible Sewag three control float av	ewage oated C x ater from the Control	Pump, 230 Volt, 3 cast Steel Housing. Unit Price \$1,586.89 In the floor to the se roller With NEMA 4 Uncludes alarm hor	Phase, S And Imp X wwage sy X Enclosen, warning	To 4" Flanged eller Factor 0.8625 = vstem, sure For Non Automatic ng light, HOA switch, and	\$2,737.3 Total \$2,737.39 \$1,175.2
38 ateg	.22 13	29 16 0012	OFK User Note: OFK	EA Installation Pump require EA	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the way Simplex Single Phase Submersible Sewag three control float sy Quantity 2,00	x x ater from	Pump, 230 Volt, 3 cast Steef Housing. Unit Price \$1,586,88 In the floor to the se roller With NEMA 4	Phase, S And Imp x wage sy	t" To 4" Flanged eller Factor 0.8625 = vstem, sure For Non Autometic ng light, HOA switch, and	\$2,737.3 Total \$2,737.39 \$1,175.2
38 ateg	.22 13 22 13 22 13	29 16 0012 Plumbing W- 29 16 0020	User Note: ork User Note:	EA Installation Pump require EA	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the way Simplex Single Phase Submersible Sewag three control float av	ewage oated C x ater from the Control	Pump, 230 Volt, 3 cast Steel Housing. Unit Price \$1,586.89 In the floor to the se roller With NEMA 4 Uncludes alarm hor	Phase, S And Imp X wwage sy X Enclosen, warning	To 4" Flanged eller Factor 0.8625 = vstem, sure For Non Automatic ng light, HOA switch, and	\$2,737.3 Total \$2,737.39 \$1,175.2
ateg	22 13 22 13 22 13 22 13	29 16 0012 Plumbing W- 29 16 0020	User Note: ork User Note:	EA Installation Pump require EA Installation Controller reconstroller reconstroller	1 HP Submersible S Discharge, Epoxy-C Quantity 2.00 ed to discharge the was Simplex Single Phas Submersible Sewag three control float sw Quantity 2.00 quired for the pump.	ewage oated C x ater from se Contr e Pump vitches,	Pump, 230 Volt, 3 ast Steef Housing. Unit Price \$1,586.89 In the floor to the se roller With NEMA 4 shouldes alarm hor Unit Price \$681.28	Phase, S And Imp X wage sy X Enclos n, warnin	To 4" Flanged siter Factor 0.8625 = retem. sure For Non Automatic ng light, HOA switch, and Factor 0.8626 =	\$2,737.3 Total \$2,737.39 \$1,175.2 Totel \$1,175.21
38 ateg	22 13 22 13 22 13 22 13	29 16 0012 Plumbing W- 29 16 0020	User Note: ork User Note:	EA Installation Pump require EA	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the way Simplex Single Phase Submersible Sewag three control float av Quantity 2,00 quired for the pump.	ewage oated C x ater from se Contr e Pump vitches,	Pump, 230 Volt, 3 cast Steel Housing. Unit Price \$1,586.88 In the floor to the se roller With NEMA 4 Includes alarm hor Unit Price \$681.28	Phase, S And Imp X wage sy X Enclos n, warnin	To 4" Flanged eller Factor 0.8625 = vstem, sure For Non Automatic ng light, HOA switch, and Factor 0.8625 =	\$2,737.3 Total \$2,737.39 \$1,175.2
ateg	22 13 22 13 22 13 22 13	29 16 0012 Plumbing W- 29 16 0020	User Note: ork User Note:	EA Installation Pump require EA Installation Controller re	1 HP Submersible S Discharge, Epoxy-C Quantity 2.00 ed to discharge the was Simplex Single Phas Submersible Sewag three control float sw Quantity 2.00 quired for the pump.	ewage oated C x ater from se Contr e Pump vitches,	Pump, 230 Volt, 3 ast Steef Housing. Unit Price \$1,586.89 In the floor to the se roller With NEMA 4 shouldes alarm hor Unit Price \$681.28	Phase, S And Imp X wage sy X Enclos n, warnin	To 4" Flanged siter Factor 0.8625 = retem. sure For Non Automatic ng light, HOA switch, and Factor 0.8626 =	\$2,737.3 Total \$2,737.39 \$1,175.2 Totel \$1,175.21
ateg	22 13 22 13 22 13 22 13	29 16 0012 Plumbing W- 29 16 0020	User Note: ork User Note: Ork	EA Installation Pump require EA Installation Controller re-	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the way Simplex Single Phase Submersible Sewag three control float sy Quantity 2,00 quired for the pump. 36" Diameter x 36" F	ewage oated C x ater from se Contr e Pump vitches,	Pump, 230 Volt, 3 cast Steel Housing. Unit Price \$1,586.88 In the floor to the se roller With NEMA 4 Includes alarm hor Unit Price \$681.28	Phase, S And Imp x wage sy X Enclose n, warnte x	To 4" Flanged eller Factor 0.8625 = vstem, sure For Non Automatic ng light, HOA switch, and Factor 0.8625 =	\$2,737.3 Total \$2,737.39 \$1,175.2 Totel \$1,175.21
ateg	22 13 22 13 22 13 22 13	29 16 0012 Plumbing W- 29 16 0020 Plumbing W- 29 33 0013	User Note: User Note: Ork User Note:	EA Installation Pump require EA Installation Controller re-	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the way Simplex Single Phase Submersible Sewag three control float sw Quantity 2,00 quired for the pump.	ewage coated C x ster from the Continue Continu	Pump, 230 Volt, 3 ast Steel Housing. Unit Price \$1,586.89 In the floor to the se roller With NEMA 4 Includes alarm hor Unit Price \$681.28 erglass Besin And Unit Price	Phase, S And Imp x wage sy X Enclose n, warnte x	To 4" Flanged alter Factor 0.8625 = stem. sure For Non Automatic ng light, HOA switch, and Factor 0.8625 = Inlet And Hub Factor	\$2,737.3 Total \$2,737.39 \$1,175.2 Totel \$1,175.21
ateg	22 13 22 13 22 13 22 13	29 16 0012 Plumbing W- 29 16 0020	User Note: User Note: Ork User Note:	EA Installation Pump require EA Installation Controller re-	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the way Simplex Single Phase Submersible Sewag three control float sy Quantity 2,00 quired for the pump. 36" Diameter x 36" F	ewage coated C x ster from the Continue Continu	Pump, 230 Volt, 3 ast Steel Housing. Unit Price \$1,586.89 In the floor to the se roller With NEMA 4 Includes alarm hor Unit Price \$681.28 erglass Besin And Unit Price	Phase, S And Imp x wage sy X Enclose n, warnte x	To 4" Flanged alter Factor 0.8625 = stem. sure For Non Automatic ng light, HOA switch, and Factor 0.8625 = Inlet And Hub Factor	\$2,737.3 Total \$2,737.39 \$1,175.2 Totel \$1,175.21
atego atego 40	22 13 22 13 22 13 22 13	29 16 0012 Plumbing W- 29 16 0020 Plumbing W- 29 33 0013	User Note: ork User Note: ork User Note:	EA Installation Pump require EA Installation Controller re-	1 HP Submersible S Discharge, Epoxy-C Quantity 2,00 ed to discharge the way Simplex Single Phase Submersible Sewag three control float sy Quantity 2,00 quired for the pump. 36" Diameter x 36" F	ewage coated C x ster from the Continue Continu	Pump, 230 Volt, 3 ast Steel Housing. Unit Price \$1,586.89 In the floor to the se roller With NEMA 4 Includes alarm hor Unit Price \$681.28 erglass Besin And Unit Price	Phase, S And Imp x wage sy X Enclose n, warnte x	To 4" Flanged alter Factor 0.8625 = stem. sure For Non Automatic ng light, HOA switch, and Factor 0.8625 = Inlet And Hub Factor	\$2,737.3 Total \$2,737.39 \$1,175.2 Totel \$1,175.21

Job Order Number:

042132.00

Job Order Title:

	Cair	lumber	Mod.	UOM	Description					Line Tota
23 - 1	leatir	ıg, Ventilatin	g, And Air	-Condition	ing (HVAC)					
41	23 0	5 53 00 0012		EA	4" Outside Diame	ter Snap-(On Plastic Marker			\$281.0
				•	Quantity	••	Unit Price		Factor	Total
				Installation	20,00	×	\$15_29	x	0.8625 #	\$281.00
			User Note:	Required for	r all piping for identifi	ication,				
ateg	ory1:	Plumbing W	ork							
42	23 Q	5 53 00 0042		EA	1-1/2" Diameter Id	entificatio	n Tag, Brass			\$26.5
					Quantity		Unit Price		Factor	Total
				Installation	4,00	×	\$7,70	×	0.8625 =	\$26.57
			User Note:	Required for	all valves for identif	ication.				
ateg	ory1:	Plumbing We	ork							
43	23 05	93 00 0084		EA	>1,000' To 2,000'.	>1-1/2" T	o 4" Piping, Hydro	static Te	esting	\$2,181.9
					Quantity		Unit Price		Factor	Total
				Installation	1.00	x	\$2,529,76	v	0.8625 =	\$2,181.92
			User Note:		test the new piping t		•	,,	v	42,101102
atego	огу1:	Plumbing Wo		•				,		·
										
ubto	tal fo	r 23 - Heatin	g, Ventilati	ing, And Ai	r-Conditioning	(HVAC)	:			\$2,489.4
6 - E	lectri	cal	, ,							
44	26 01	20 00 0003		EA	Lock Out/Tag Out	Breaker (r Motor Starter			\$54.4
				Plant	Quantity					
					ot or a true la		Unit Price		Factor	Total
				Installation	2.00	x	Unit Price \$31.54	x	Factor 0.8625 =	\$54.41
	-		Usar Note:		•		\$31.54		0.8625 =	
atego	ory1:				2.00		\$31.54		0.8625 =	
	-,	Work		Lock out pov	2.00 ver and control to all	ow work o	\$31.54 on a system that w	ill remair	0.8625 = n live.	\$54.41
	-,				2.00 ver and control to all 50', 10-4, SEOOW	ow work o	\$31.54 on a system that w	ill remair	0.8625 = n live.	\$54,41 \$7,394.5
	-,	Work		Lock out pov	2.00 ver and control to all 50', 10-4, SEOOW Quantity	ow work o	\$31.54 on a system that w in Cord Reel (Ree Unit Price	ill remair	0.8625 = 1 live. 050 104 X 1) Factor	\$54,41 \$7,394.5 Total
	-,	Work	itroī	EA	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00	, Extension	\$31.54 on a system that w in Cord Reel (Ree Unit Price \$1,428.90	ill remair Icraft L 7	0.8625 = 1 live. 050 104 X 1) Factor 0.8625 =	\$54,41 \$7,394.5
45	26 05	Work 19 16 0205	troi User Note:	EA	2.00 ver and control to all 50', 10-4, SEOOW Quantity	, Extension	\$31.54 on a system that w in Cord Reel (Ree Unit Price \$1,428.90	ill remair Icraft L 7	0.8625 = 1 live. 050 104 X 1) Factor 0.8625 =	\$54,41 \$7,394.5 Total
45	26 05	Work 19 16 0205 Power & Con	troi User Note:	EA	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00	, Extension	\$31.54 on a system that w in Cord Reel (Ree Unit Price \$1,428.90	ill remair Icraft L 7	0.8625 = 1 live. 050 104 X 1) Factor 0.8625 =	\$54,41 \$7,394.5 Total
45	28 05 pry1:	Work 19 16 0205 Power & Con Work	troi User Note:	EA Installation	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe	, Extension x r ejector.	\$31.54 on a system that w in Cord Reel (Ree Unit Price \$1,428.80 Existing must be r	Icraft L 7	0.8625 = n live. 050 104 X 1) Factor 0.8625 =	\$54,4† \$7,394.5 Total \$7,394.56
45 atego	28 05 pry1:	Work 19 16 0205 Power & Con	troi User Note:	EA	2.00 ver and control to all 50', 10-4, SEOOW Quantity 6,00 or. Three required pe	, Extension x r ejector.	\$31.54 on a system that w in Cord Reel (Ree Unit Price \$1,428.80 Existing must be r	Icraft L 7	0.8625 = 1 live. 050 104 X 1) Factor 0.8625 =	\$54,41 \$7,394.5 Total
45 atego	28 05 pry1:	Work 19 16 0205 Power & Con Work	troi User Note:	EA Installation	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe	, Extension x r ejector.	\$31.54 on a system that w in Cord Reel (Ree Unit Price \$1,428.80 Existing must be r	Icraft L 7	0.8625 = n live. 050 104 X 1) Factor 0.8625 =	\$54,4† \$7,394.5 Total \$7,394.56
45 atego	28 05 pry1:	Work 19 16 0205 Power & Con Work	troi User Note:	EA Installation	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe #1/0 AWG Cable - In Conduit	, Extension x r ejector.	\$31.54 on a system that w on Cord Reel (Ree Unit Price \$1,428.80 Existing must be r IN-THVVN 600 Vo	Icraft L 7 x emoved.	0.8625 = n live. 050 104 X 1) Factor 0.8625 = r, Single Stranded, Placed	\$54,4† \$7,394.5 Total \$7,394.56 \$8,066,3
45 atego	28 05 pry1:	Work 19 16 0205 Power & Con Work	User Note: troi	EA	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe #1/0 AWG Cable - In Conduit Quantity 2.00	x rejector.	\$31.54 on a system that w on Cord Reel (Ree Unit Price \$1,428.90 Existing must be r	Icraft L 7 x emoved.	0.8625 = n live. 050 104 X 1) Factor 0.8625 = r, Single Stranded, Placed	\$54,4† \$7,394.5 Total \$7,394.56 \$6,066.3
45 atego	28 05 Pry1: 28 05	Work 19 16 0205 Power & Con Work 19 16 0533	User Note: trol	EA Installation Ejector power MLF	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe #1/0 AWG Cable - In Conduit Quantity 2.00	x rejector.	\$31.54 on a system that w on Cord Reel (Ree Unit Price \$1,428.80 Existing must be r IN-THVVN 600 Vo	Icraft L 7 x emoved.	0.8625 = n live. 050 104 X 1) Factor 0.8625 = r, Single Stranded, Placed	\$54,4† \$7,394.5 Total \$7,394.56 \$6,066.3
45 45 46 48	26 05 Pry1: 28 05	Work 19 16 0205 Power & Con Work 19 16 0533	User Note: trol	EA Installation Ejector power MLF	2.00 ver and control to all 50', 10-4, SEOOW Quantity 6,00 or. Three required pe #1/0 AWG Cable - In Conduit Quantity 2.00 r.	Extension x r ejector. Type THF	\$31.54 on a system that w on Cord Reel (Ree Unit Price \$1,428.90 Existing must be r 1N-THVVN 600 Vo Unit Price \$3,516,72	Icraft L 7 x emoved.	0.8625 = n live. 050 104 X 1) Factor 0.8625 = r, Single Stranded, Placed	\$7,394.5 Total \$7,394.56 \$8,066.3 Total \$6,066.34
45 atego	26 05 Pry1: 28 05	Work 19 16 0205 Power & Con Work 19 16 0533 Power & Con Work	User Note: trol	EA Installation Ejector power MLF Installation Ejector power	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe #1/0 AWG Cable - In Conduit Quantity 2.00 r. Key Interlock All Pe	Extension x r ejector. Type THF	\$31.54 on a system that w on Cord Reel (Ree Unit Price \$1,428.80 Existing must be r IN-THVVN 600 Vo Unit Price \$3,516,72	Icraft L 7 x emoved.	0.8625 = n live. 050 104 X 1) Factor 0.8625 = r, Single Stranded, Placed Factor 0.8625 =	\$54,4† \$7,394.5 Total \$7,394.56 \$6,066.3 Total \$6,066.34
45 45 46 48	26 05 Pry1: 28 05	Work 19 16 0205 Power & Con Work 19 16 0533 Power & Con Work	User Note: trol	EA	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe #1/0 AWG Cable - In Conduit Quantity 2.00 r. Key Interlock All Po	Extension X rejector. Type THF X	\$31.54 on a system that w on Cord Reel (Ree Unit Price \$1,428.80 Existing must be r IN-THVVN 600 Vo Unit Price \$3,516,72 kers - Factory Inst	ill remain icraft L 7 x emoved. It Coppe	0.8625 = n live. 050 104 X 1) Factor 0.8625 = 7, Single Stranded, Placed Factor 0.8625 =	\$54,4† \$7,394.5 Total \$7,394.56 \$6,066.3 Total \$6,066.34
45 atego	26 05 Pry1: 28 05	Work 19 16 0205 Power & Con Work 19 16 0533 Power & Con Work	User Note: troi User Note: troi	EA Installation Ejector power MLF Installation Ejector power EA Installation	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe #1/0 AWG Cable - In Conduit Quantity 2.00 r. Key Interlock All Po Quantity 6,00	Extension X If ejector. Type THF X Dwer Bree X	\$31.54 on a system that w on Cord Reel (Ree Unit Price \$1,428.80 Existing must be r IN-THVVN 600 Vo Unit Price \$3,516,72 kers - Factory Inst Unit Price \$244.31	ill remain icraft L 7 x emoved. It Coppe	0.8625 = n live. 050 104 X 1) Factor 0.8625 = r, Single Stranded, Placed Factor 0.8625 =	\$54,4† \$7,394.5 Total \$7,394.56 \$6,066.3 Total \$6,066.34
45 atego	28 05 28 05 28 05 ry1:	Work 19 16 0205 Power & Con Work 19 16 0533 Power & Con Work	User Note: trol User Note: trol	EA Installation Ejector power MLF Installation Ejector power EA Installation	2.00 ver and control to all 50', 10-4, SEOOW Quantity 8,00 or. Three required pe #1/0 AWG Cable - In Conduit Quantity 2.00 r. Key Interlock All Po	Extension X If ejector. Type THF X Dwer Bree X	\$31.54 on a system that w on Cord Reel (Ree Unit Price \$1,428.80 Existing must be r IN-THVVN 600 Vo Unit Price \$3,516,72 kers - Factory Inst Unit Price \$244.31	ill remain icraft L 7 x emoved. It Coppe	0.8625 = n live. 050 104 X 1) Factor 0.8625 = 7, Single Stranded, Placed Factor 0.8625 =	\$54,4† \$7,394.5 Total \$7,394.56 \$6,066.3 Total \$6,066.34

Job Order Number: 042132,00

Job Order Title:

CCB Install Floor Drains-Penthouse & Equipment Rooms

Rec#	CSIN	lumber	Mod.	UOM	Description		Line Tota
26 - E	Electr	ical				- thinks	
48	26 24	19 00 0270		EA	Control Circuit Transformer 60 Hertz, Size 1, 2,	50 VA Standard	\$486.0
					Quantity Unit Price	Factor	Total
				Installation	6.00 _X \$93.93	x 0.8625 =	\$486.09
			User Nate:	Ejector and	stem control. Three required per ejector. Two ej	ectora.	
Catego	ory1:	Power & Con Work	trol				
49	28 24	19 00 0273		EΑ	Control Circuit Transformer 60 Hartz, All Sizes,	Extra 50 VA	\$532,8
	:				Quantity Unit Price	Factor	Total
				Installation	6,00 _X \$102.97	x 0,8625 *	\$532.87
			User Note:	Ejector and	stem control, Three required per ejector, Two eje	ectors.	
Catego	ory1:	Power & Con Work	trol				
50	26 24	19 00 0302		EA	Wiring To Common Control Circuit Transformer		\$292.9
		•			Quantity Unit Price	Factor	Total
				installation	6.00 x \$58.80	x 0.8625 =	\$292.91
			User Note:	Ejector and	stem control. Three required per ejector, Two eje	••	
atego	ory1:	Power & Con Work					
51	28 24	19 00 0306		EA	Ring Terminals Power		\$292,
					Quantity Unit Price	Factor	Total
				Installation	5:00 x \$58.60	x 0.8625 =	\$292,91
atego	ory1;	Power & Cont Work	User Note: troi	Ejector and	stem control. Three required per ejector. Two eje	ectors,	
52	28 24	19 00 0316		EA	Control Relays, 600 Volt, 4 Pole		\$1,739,1
					Quantity Unit Price	Factor	Total
				Installation	6,00 x . \$336,07	x 0.8625 =	\$1,739.18
atego	ry1:	Power & Cont Work		Ejector and	stem control. Three required per ejector. Two eje	actors.	
53	26 27	26 00 0068		EA	Pin And Sleave, 30 Amp, 277/480 Volt Power Re	eceptacles And Box	\$625.5
					Quantity Unit Price	Factor	Total
				Installation	8,00 x \$120,87	x 0.8625 =	\$625.50
atego	•	Power & Cont Work		Ejector powe	Three required per ejector. Two ejectors,		
ubtot	al for	26 - Electric	al:				\$18,749.0
ropos	est Ta	ital					
·opus	3a1 10	rial					\$354,618.1

This proposal total represents the correct total for the proposal. Any discrepancy between line totals, sub-totals and the proposal total is due to rounding of the line totals and sub-totals.

The Percent of NPP on this Proposal:

0.00%



HVAC Construction & Service

January 31, 2017

Ms. Sheila V. Atkins
Project Director - Bureau of Asset Management
Cook County - Capital Planning & Policy
69 W. Washington
Suite 3000
Chicago, Illinois 6060

RE: Proposal - Engineering Work

CCB Install Floor Drains-Penthouse & Equipment Rooms

Criminal Courts Building

2700 S. California Avenue, Chicago, Illinois 60608

Work Order #042132.00

Dear Ms. Atkins,

Please accept our proposal for the engineering services required for the above referenced project.

The goal of this project is to provide a drainage system for the east and west sides of the Penthouse above the courtrooms. This is to be accomplished via pouring new levels of concrete over the existing floors on the east and west sides of the Penthouse; adding one sewage ejector system to the existing plumbing piping drainage system on each side of the Penthouse resulting in a total of two systems; provision of electrical power work; and provision of stand-alone control of the ejectors utilizing float switches.

This proposal includes the following work:

1.	Review and approval of the proposed concrete, plumbing, electrical and control work;
	a. (5) Hrs x \$150/Hr\$750
· 2.	Field survey to verify existing conditions: (5) Hrs x \$150/Hr
3.	Details: (5) Hrs x \$150/Hr
4.	Code review: (5) Hrs x \$150/Hr
5.	Site visits: (9) Hrs x \$150/Hr
6.	Specifications of systems and equipment: (5) Hrs x \$150/Hr
7.	Construction assistance: (6) Hrs x \$150/Hr900
	To assist the contractor as needed to advise and inspect the installation.
8.	TOTAL PRICE\$6.000

All of the above services are provided by a licensed professional engineer.

We trust the above meets with your approval. If you have any questions and/or comments, then please feel free to contact us.


Thank you.

Sincerely,

--S Mechanical, Inc.

Dan Nolan

Business Manager



Work Order Number:

042132.00

Contractor: Cook County - S Mechanical

Work Order Title:

CCB Install Floor Drains-Penthouse & Equipment Rooms

Date:

January 24, 2018

Subcontractor and M/W/SBE Estimate

Following is the proposed list of minority owned, woman owned and non-minority subcontractors and material suppliers proposed for the above Work Order. This estimate is submitted with our final Work Order Proposal in the amount of \$354,618.16.

Contractor	Duties	Trade	M/W/SBE Status	Total \$	M/W/SBE \$	% of Project
G&V Construction Co, Inc.	Concrèté work.	S	W	\$80,782.00	\$80,782.00	22.78%
J.M. Palcurr, Inc.	Power and control work.	S	M	\$15,000.00	\$15,000.00	4.23%
J.S.R. Enterprises, Inc.	Plumbing work,	s	M	\$25,000.00	\$25,000.00	7.05%
S Mechanical	Concrete work, dumpster, coring and startup.	\$	N	\$233,836.16	\$0.00	0.00%

Trades - S: Subcontractor; M: Material Supplier

MWBE's - M: Minority; W: Women; N: Non M/WBE

\$354,618.16

\$120,782.00

34.06%

Total MBE Subcontractor Participation Scheduled Total MBE Supplier Participation Scheduled	\$40,000,00 \$0.00	11.28% 0.00%	\$40,000.00	MBE Total
Total WBE Subcontractor Participation Scheduled Total WBE Supplier Participation Scheduled	\$80,782.00 \$0.00	22,78% 0.00%	\$80,782.00 22.78%	WBE Total
Total SBE Subcontractor Participation Scheduled Total SBE Supplier Participation Scheduled	\$0.00 \$0.00	0.00% 0.00%	\$0.00	SBE Total
Total M/W/SBE Participation Scheduled	\$120,782.00	34.06%	_	

(Contractor) Project Manager

Dave Amacher - S Mechanical Project Manager

PETITION FOR REDUCTION/WAIVER OF MBE/WBE PARTICIPATION - FORM 3

A. <u>BIDDER</u>	VPROPOSER HEREBY REQUESTS:		
	FULL MBE WAIVER		FULL WBE WAIVER
>	REDUCTION (PARTIAL MBE and/or WBE PART	'ICIPAT	ION)
	% of Reduction for MBE Participation% of Reduction for WBE Participation		
B. <u>REASOI</u>	N FOR FULL/REDUCTION WAIVER REQUEST		
	poser shall check each item applicable to its reason tion shall be submitted with this request.	on for a	a waiver request. Additionally, supporting
(1)	Lack of sufficient qualified MBEs and/or WBEs capab by the contract. (Please explain)	le of pro	oviding the goods or services required
X (2)	The specifications and necessary requirements for pe economically infeasible to divide the contract to enable accordance with the applicable participation. (Please	le the c	ontractor to utilize MBEs and/or WBEs in
(3)	Price(s) quoted by potential MBEs and/or WBEs are a doing business and would make acceptance of such taking into consideration the percentage of total contribid. (Please explain)	MBE an	d/or WBE bid economically impracticable,
(4)	There are other relevant factors making it impossible of WBE firms. (Please explain)	or econo	omically infeasible to utilize MBE and/or
C. <u>GOOD F</u>	AITH EFFORTS TO OBTAIN MBE/WBE PARTICIPAT	ION	
(1)	Made timely written solicitation to identified MBEs and and provided MBEs and WBEs with a timely opportuterms and conditions of the proposal to enable MBEs solicitation. (Attach of copy written solicitations m	nity to r and W	eview and obtain relevant specifications,
(2)	Used the services and assistance of the Office of Cor	ntract C	compliance staff. (Please explain)
(3)	Timely notified and used the services and assistance organizations. (Attach of copy written solicitations		
(4)	Followed up on initial solicitation of MBEs and WBEs business. (Attach supporting documentation)	to deter	rmine if firms are interested in doing
<u>(5)</u>	Engaged MBEs & WBEs for direct/indirect participation	n. (Plea	ase explaîn)

D. OTHER RELEVANT INFORMATION

Attach any other documentation relative to Good Falth Efforts in complying with MBE/WBE participation.

Due to the small number of subcontractors required for this project, we are not able to meet our MBE goal. However, we are aware of this shortfall and will make efforts on future projects to meet the goal. We plan to meet the goal at the end of the contract.



Cook County Office of Planning & Policy 69 W Washington Chicago, IL 60602

Date: January 24, 2018

Sub-Order Total:

\$354,618.16

Disclosure of Retained Parties

A. Definitions and Disclosure Requirements

- 1. As used herein, the term "Contractor" means a person of entity who has any contract lease with the County of Cook,
- Pursant to Executive Order 97-1, every city contract and tease must be accompanied by a disclosure statement Providing certain information and attorneys, tobbyists, accountants, consultants, sonsultants, subcontractors, and other persons
- The Contractor is not required to disclose employees who are paid solely through the Contractor's regular payroll.
- 4. "Lobbylet" means any person (a) who for companisation or on behalf of any person other than himself undertakes to influence any legislative or administration, action, or (b) any part or whose duties as an employee of another includes undertaking to influence any legislative or administrative action.

B. Certification

Contractor hereby cartifies as follows:

- 1. This Disclosure relates to the following transaction:
- Project name: 042132.00 CCB Install Floor Drains-Penthquae & Equipment Rooms
- 3. Name of Contractor: Cook County S Mechanical

EACH AND EVERY attorney, lobbylist, accountent, consultant, subcontractor, or other person retained or anticipated to be retained by the Contractor with respect to or in connection with the contract or lease. Is listed below (attach additional pages if necessary):

Name.	Business Address	MBE WBE or Non	RelationShip (attorney,lobbylet, aubcontractor,etc.)	FEE(indicate whether paid \$ or estimated)
J.S.R. Enterprises, Inc.	4931 W. 173RD St. Unit D GOUNTRY CLUB HILLS, IL, 60478	MBE	Subcontractor	\$25,000.00 Est.
J.M. Polcum, Inc.	3024 S 25th Street Broadview, IL, 60155	MBE	Subcontractor	\$15,000,00 Est.
S Mechanical	16420 S. Kilboum Ave. Suite B OakForfest, IL, 60452	Non	Subcontractor	\$235,387.18 Est
G&V Construction Co, Inc.	5239 W. Diversey Ave, Ste 201 Chicago, IL, 60639	WBE	Subcontractor	\$60,782.00 Est.

CHECK HERE IF NO SUCH PERSONS HAVE BEEN RETAINED OR ARE ANTICIPATED TO BE RETAINED.

- 4. The Contractor Understands and agrees that the city may rely on the information provided herein and that providing any false incomplete or inacquirance information shall constitute default unique the contract and may result in termination of the contract or lease
- 5. The Contractor understands and agrees that in any case in which the Contractor is uncertain whether a disclosure is required under the Executive order, the Contractor must either ask the by whether disclosure is programed or make the disclosure.

Under the Tenalities of perjury. Leartify that I am authorized to execute this Disclosure on behalf of the Contractor that the information disclosed herein is true and compete and that no relevant information has been githered.

O1/24/2018

Signature

Dave Amacher

Project Manager

Name (Type or Print)

Subscribed and sworn to before me

this 25th day of January 20 18

JANICE KEATING
NOTARY PUBLIC - STATE OF ILLINOIS
MY COMMISSION EXPIRES:03/31/20

OFFICIAL SEAL

Disclosure Statement

Cn	ńk	Co	unt	ΰ

SECTION 7- EXHIBITS

EXHIBIT A-MBE/WBE UTILIZATION PLAN

BIDDER/PROPO Conditions - Sec		TES that all MBE/M	BE firms included in this	Plan are certified	MBES/WBES b	y at least one of the entitles liste	d in the General
		MBE/WBE STATU	S: (check the appropriate	e line)			
	Bldd	ler/Proposer is a co	ertified MBE or WBE firm	ı. (If so, attach cop	y of appropria	te Letter of Certification)	
dise	Cert	ification, à copy of l	Venture and one or more , oint Venture Agreement s John Venture Affidavit-ava	learly describing th	e role of the M	NBEs or WBEs. (If so, attach copies of BE/WBE firm(s) and its ownership i p/contractopmoliance)	Letter(s) of nterest in the Joint
	Bidd dire	ier/Proposer la not ectly or indirectly it	a certified MBE of W8E the performance of the	firm, nor a Joint \ Contract, (IF so,)	enture with M complete Secti	BE/WBE partners, but will utilize ons it below and the Letter(s) of I	MBE and WBE firms eith intent-Form 2).
и. [X Dire	ct Participation of	MBE/WBE Firms		Indirect Partic	cipation of MBE/WBE Firms	
achieve i achieve i Partidpat	Direct Participal Direct Participa ion be considere	tion at the time tion have been d.	e of Bid/Proposal sul	britssion. Indirec er written doct	t Participatio imentation o	ell include documentation on will only be considered a f Good Faith Efforts is rec	after all efforts to
p	MBE/WBE Firm:	J.S.R. Enterprises,	lnc.		······································		
	Address:	4931 W. 173rd St	. Unit D, Country Club Hi	ilis, il 60478			
ŧ	E-Mali	stoberts@istent.c	om	· · · · · · · · · · · · · · · · · · ·			
•	Contact Person:	Jerry Robert			Phone: 708	206-1800	***************************************
1	Doller Amount Pa	rtidpation:\$	25,000				
-į	Percent Amount	of Participation:	7,01			wije nije was i pojenia na od ose je nije i same ko od	
	*Letter of Intent *Letter of Certific			Yes X Yes X		No	<u>.</u>
!	MBE/WBE Firm:	G&V Construction	n Ço, Inc.			<u> </u>	
¥	Address:	5239 W Diversey	Ave., Suite 201, Chicago	, IL 60639			
1	E-Mall	anna@gvconsttu	ctionco.com				
	Contact Person:	Anna Favuz	1.		Phone: 630	-595-6474	· · · · · · · · · · · · · · · · · · ·
i	Dollar Amount Pa	articipation: \$	80,782.00				
	Percent Amount	of Participation:	22.78%				
	*Letter of Intent *Letter of Certific	attached? cation attached?		Yes X		No	- -

^{*} Letter(s) of intent and current Letter of Certification <u>must</u> be submitted at the time of bid.

ok County	-					
MBE/WBE Firm:	JM Poicurr, Inc.			· · · · · · · · · · · · · · · · · · ·		
Address:	3024 S. 25th Av	enue, Broadview,	IL 60155			
E-Mail	john@jmpolcur	r.com				
Contact Person:	John Marq	uez		Phone: <u>70</u>	8-450-1156	
Dollar Amount P	articipation; \$	15,000				
Percent Amount	of Participation:	4.21	,	·		
*Letter of Intent *Letter of Certific				X	No	
MBE/WBE Firm:			·			
Address:						
E-Mail						
Contact Person:						
Dollar Amount Pa	articipation: \$					
Percent Amount	of Participation:					
*Letter of Intent *Letter of Certific			Yes	X X	No	
MBE/WBE Firm:					***	
Address:				· · · · · · · · · · · · · · · · · · ·		
E-Mail						
Contact Person:				Phone:		
Dollar Amount Pa	articipation: \$					
Percent Amount	of Participation:		,			
*Letter of Intent *Letter of Certific			Yes		No	
MBE/WBE Firm:						
Address:	_					
E-Mail				•		
Contact Person:				Phone:		
Dollar Amount Pa						
Percent Amount						
*Letter of Intent: *Letter of Certific	attached?				No	

Subcribed and sworn before me

January

SEAL

200

this 24th day of

Notary Public

OFFICIAL SEAL JERRY C ROBERTS III MY COMMISSION EXPIRES: 10/04/18

NOTARY PUBLIC - STATE OF ILLINOIS _{ѵѵѵѵ}ѵѵѵѵѵѵѵѕ҃ҍѻҭӀ҅ѲЍӋ҇ѴѲӾҤӀВѬҍ Subscribed and sworn before me

this 24th day of

Notary Public

Janice Keating

SEAL

OFFICIAL SEAL JANICE KEATING NOTARY PUBLIC - STATE OF ILLINOIS MY COMMISSION EXPIRES:03/3M20 20

EXHIBIT G - LETTER OF INTENT BETWEEN PRIME CONTRACTOR AND MBE/WBE SUBCONTRACTOR OR SUPPLIER

COOK COUNTY, ILLINOIS LETTER OF INTENT BETWEEN PRIME CONTRACTOR AND MBE/WBE SUBCONTRACTOR OR SUPPLIER

			P. Eminman				
ontract Title	CCB Install Floor Dr Rooms	ams-reninouse	or referibition	Contract Num	ber: <u>042132.0</u>	0	
rime proposer:	S Mechani	ical Inc.	- Table 11 - 11 - 11 - 11 - 11 - 11 - 11 - 11				
me hickore.	3 Micchall	ion in the			<u> </u>		
ddress	16420 S Kilboum /	lve.			Oak Forest	l L	60452
	Street				City	State	Zip Code
elephone:	708-535-3600		FAX:	708-535-6655	e mail:	damacher@smechanical.com	
roposed Contra	ect amount \$: 3	54,618.16		//- In-			
roposed subcor	ntract amount: \$:	25,000.00				· · · · · · · · · · · · · · · · · · ·	
ype of agreeme	ent: X	lump sum		hourly rate	unit price	,	
ABE/WBE subco	ontractor or supplier:	J.S.R. Enter	prises				
ddress 49	931 W 173rd Street U	nit D			Country Club H	ilis IC.	60478
	Street				City	State	Zip Code
elephone:	708-206-	1.800	FAX	Jerry Roberts	e mail:	sroberts@jsrer	nt.com
lumbing Work							· · · · · · · · · · · · · · · · · · ·
Plumbing Work prin for	me proposer and the	e MBE/WBE lis	n the prime	nereby agree that upo Contractor and Cook Ited above.	n the execution of County, the MBI	of a Contract E/WBE will	
Plumbing Work prir for per	me proposer and the	e MBE/WBE lis	n the prime	Contractor and Cook	County, the M8I	of a Contract F/WBE will	
Plumbing Work prir for per	me proposer and th the above-named p form the scope of w (BE/WBE	e MBE/WBE lis	n the prime	Contractor and Cook ited above.	County, the M8F	of a Contract E/WBE will	
Plumbing Work prir for per M J.S.R. Enterprise	me proposer and the the above-named p form the scope of w ABE/WBE	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook sted above. Prime Propos	County, the MBI ser , In (1)	of a Contract E/WBE wifl	
Plumbing Work prir for per M J.S.R. Enterprise	me proposer and the the above-named p form the scope of w ABE/WBE	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook ited above. Prime Propose S Mechanical	County, the MBI ser , In (1)	of a Contract E/WBE wifl	
Plumbing Work prir for per M	me proposer and the the above-named p form the scope of w ABE/WBE	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook ited above. Prime Propose S Mechanical	County, the MBI ser , In (1)	of a Contract E/WBE wifl	Im
Plumbing Work prir for per M I.S.R. Enterprise Name of Fin	me proposer and th the above-named p form the scope of w MBE/WBE	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook sted above. Prime Propos <u>S Mechanical</u> Name of	County, the MBI ser , In (1)	of a Contract	Im
Plumbing Work prir for per M.S.R. Enterprise Name of Fin	me proposer and the the above-named proposer and the form the scope of water the scope of	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook sted above. Prime Propos S Mechanical Name of By: Signature Dave Amach	County, the MBE	of a Contract E/WBE wifl	Im
Plumbing Work prir for per M J.S.R. Enterprise	me proposer and the the above-named proposer and the form the scope of wheeless	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook sted above. Prime Propos S Mechanical Name of By: Signature	County, the MBE	of a Contract E/WBE will	Im
Plumbing Work print for per No. S.R. Enterprise Name of Fire Signature Sharon Roberts Print Name	me proposer and the the above-named proposer and the form the scope of wheeless	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook sted above. Prime Propos S Mechanical Name of By: Signature Dave Amach Print Name Project Manie	county, the MBE	of a Contract E/WBE will	Im.
rlumbing Work print for per No.S.R. Enterprise Name of Finit Name Print Name	me proposer and the the above-named proposer and the form the scope of wheeless	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook sted above. Prime Propos S Mechanical Name of By: Signature Dave Amach	county, the MBE	of a Contract E/WBE wifl	Im
Plumbing Work print for per N J.S.R. Enterprise Name of Fin By: Signature Sharon Roberts Print Name	me proposer and the the above-named proposer and the form the scope of wheeless	e MBE/WBE lis roject betwee vork for the pri	n the prime	Contractor and Cook sted above. Prime Propos S Mechanical Name of By: Signature Dave Amach Print Name Project Manie	county, the MBE	of a Contract E/WBE will	/m

		•		
STATE OF	~		STATE OF IL	
COUNTY OF COO	K		COUNTY OF Cook	
SUBSCRIBED AND SWORN TO) before me on the		SUBSCRIBED AND SWORN TO b	efore me on the
	,	20 <u>2018</u> .		, 20 <u>2018</u> .
1	JA			
Notary Public			Notary Public	N Co
(NANCO AND	Je gramma	My Roberts	V	e Keating
Printed Wolf of Wolf o	TS III OF ALREQUIRED BY INS	0	Printed Name of Notary OF/AND IN CONJUNCTION WIT	OFFICIAL SEAL TH THE JANICE KEATING NOTARY PUBLIC - STATE OF ILLINOI
TO: County of Cook			₩.	MY COMMISSION EXPIRES:03/31/20
BID FOR:			***	,
BID DOCUMENT NUMBER:		в	ID OPENING DATE:	
We deposit (subject to all co	nditions of said proposal)	the following described	deposit check:	
() Cashiers Check	() Bank Draft	() Other		
Drawn on:	,	of:		
Drawn dii.	BANK		СПУ	STATE
Draft or Check Number:		Date:		in distri
Amount: \$,		
Submitted by:				·
		BIDDER'S NAME		
		STREET ADDRES	S	
CITY		STATE		ZIP CODE
		DO NOT WRITE IN THI	E SPACES BELOW	
The Above Described Deposi	t Check is:	•		

SECTION 7 - EXHIBITS

May 2015

Cook County

210

EXHIBIT I - SUBCONTRACTOR'S CERTIFICATION CONCERNEING LABOR STANDARDS AND PREVAILING WAGE REQUIREMENTS

То	(Contractor):			Date: 1/24/20	018		
	S Mechanic 16420 S Kilk Oak Forest,	pourn Avenue		Project Number	r:	042132.00	
	Oak Turesty	16 504-52		Project Name:	CCB Install . Equipment	lf Floor Drains-Penthouse at Rooms	
1.	The undersigne	ed, having executed a Contract with		S Mechar (Contr			
		fo	r <u>Pl</u>	umbing Work		(Nature of work)	
			_in the amount of \$	25,000.00			
	in the construc	tion of the above-identified prject, certifies The Labor Standards provisions fo the Co		n are included in t	the		
	(-/	aforesaid Contract.					
	(b)	Neither he nor any firm, corporation, part substantial interest is designated as an in General of the United States pursuant to Secretary of Labor, Part 5 (29 CFG, Part 5) Bacon Act, as amended [40 W.S.C. 276a-2	eligible Contractor by Section 5.6(b) of the F) or pursuant to Section	the Comptroller Regulations of the			
٠	(c)	No part of the aforementioned Contract h Subcontractor if such Subcontractor or ar which such Subcontractor has a substanti Contractor pursuant to any the aforesaid	ny firm, corporation, p al interest is designate	artnership or asso ed as an ineligible	ociation in		
2.	days after	to obtain and forward to the Contractor, for the execution of any lower subcontract a St dards and Prevailing Wage Requirements, e	ubcontractor's Certific	ation Concerning			
3.	The workm	en will report for duty on or about	3/5/201	18	_(date)		

)	the legal name and t	he business address of the undersigned a	re:	
	J.S.R. Enterprise: 4931 W 173rd S Country Club Hil	treet Unit D		
)	The undersigned is (check one):			
	Sole Proprie	etorship		
	X Corpor			
	The Name and address of the owner partners or officers of the undersigned are:			
	Name	Title	ADDRESS	
	Jerry Roberts	President	PO Box 146, Matteson, IL 60443	
	Sharon Roberts	Vice-President	PO Box 146, Matteson, IL 60443	
				
	•			
				-
	ACTOR: J.S.R. Enterp	rises		
URE	: <u>Wave</u> 24/2018	-Vare		
	2/1/2019			

Vendor Information



Vendor Information

Business Name

J.S.R. Enterprises, Inc.

Owner

Jerry Roberts

Address

4931 W. 173RD St. Unit D

> Map This Address

COUNTRY CLUB HILLS, IL 60478

708-206-1800

Fax Email 708-206-1879 sroberts@isrent.com

Wabsite

http://www.isrent.com

Certification Information

Certifying Agency

City of Chicago

Certification Type

MBE - Minority Business Enterprise

Certification Date

4/21/2017

Renewai Date Expiration Date 2/15/2018

Certified Business

2/15/2018

Description

NAICS 237110 Water and Sewer Line and Construction NAICS 238220 Plumbing contractors NAICS 238910 Site Preparation Contractors (Wrecking, Demolition, and Excavation) NAICS 423720 Plumbing, Heating Equipment and Supplies

(Wholesalers)
NAICS 531210 Offices of Real Estate Agents and Brokers
NAICS 531390 Other Activities Related to Real Estate

Commodity Codes

Code	Description
NAICS 237110	Water and Sewer Line and Related Structures Construction
NAICS 238220	Plumbing contractors
NAICS 238910	Excavation contractors
NAICS 238910	Site Preparation Contractors
NAICS 423720	Plumbing and Heating Equipment and Supplies (Hydronics) Merchant Wholesalers
NAICS 531210	Offices of Real Estate Agents and Brokers

Other Activities Related to Real Estate

Additional Information

NAICS 531390

Customer Support

Print This Page

Copyright @ 2018 B2Gnow. All rights reserved.

Vendor Information

emaN aseniau6 Owner

J.S.R. Enterprises, Inc. Jerry Roberts

Address
> Map This Address

4931 W. 179RD St. Unit D COUNTRY CLUB HILLS, IL 69478

Phone Fax

708-206-1800 708-206-187B Emall arobarts@larant.com Website http://www.larent.com

Certification information

Cartifying Agency

City of Chicago

Certification Type

MBE - Minority Business Enterprise

Cartification Date 4/21/2017 Renewal Date. 2/15/2018 Expiretion Date 2/15/2018

Certified Business Description

2/13/2016

AAIGS 22/110 Weber and Sewer Line and Construction
NAIGS 22/110 Weber and Sewer Line and Construction
NAIGS 23/110 Site Preparation Contractors (Wrecking,
NAIGS 23/110 Site Preparation Contractors (Wrecking,
Demolition, and Excavation)
NAIGS 42/120 Plumbing, Heating Equipment and Bupplies
(Wholesalars)
NAIGS 53/1210 Offices of Real Estate Agents and Brokers
NAIGS 53/1210 Offices of Real Estate Agents and Erokers
NAIGS 53/1390 Other Activities Releiged to Real Estate

Commodity Codes

Code

NAICS 23711D

Water and Sewar Line and Related Structures Construction

NAICS 258220 Plumbing contractors NAICS 238910

Excevation contractors

NAICS 238910

Site Preparation Contractors

NAICB 428720

Plumbing and Heating Equipment and Supplies (Hydronics) Marchant Wholesaters

NAICS 531210 Offices of Real Extate Agents and Strokers Other Activities Related to Real Estate

NAICS 531390

Additional information

Customer Support
Copyright @ 2018 B2Gnow, All rights reserved.

Print This Page

May 2015

200

SECTION 7- EXHIBITS

EXHIBIT G - LETTER OF INTENT BETWEEN PRIME CONTRACTOR AND MBE/WBE SUBCONTRACTOR OR SUPPLIER

COOK COUNTY, ILLINOIS LETTER OF INTENT BETWEEN PRIME CONTRACTOR AND MBE/WBE SUBCONTRACTOR OR SUPPLIER

Contract Title	CCB Install Floor Rooms	Drains-Penthouse &	& Equipmen	t Contract Nur	nber: <u>042132</u> .	60	
Prime proposer:	S Mecha	inical, inc.	,		حيناب خارتاية أو بالروثية الماسانية.		
Address	16420 \$ Kilbourn	Ave.		~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~	Oak Forest	IL. State	60452
Telephone:	Street 708-535-3600	<u> </u>	FAX:	/08-53S-6655	City e mail:	State damacher@smechanical.com	Zip Code
Proposed Contra	ctamount\$: 3	54,618.16	,,	· · · · · · · · · · · · · · · · · · ·)	· · · · · · · · · · · · · · · · · · ·
Proposed subcor	ntract emount: \$:	80,782.00		 			
Type of agreeme	nt X	lump sum	1	nourly rate	unit price		
MBE/WBE subco	entractor or supplie	er: G&V Constr	uction Co In	Ç		·	
Address 52	39 W Diversey Ave	. Suite 201			Chicago	ı.	6063 <u>9</u>
Telephone:	Street 630-59:		FAX:	Anna Favuzzi	City e mail:	State anna@avconstructin	Zip Code
for		l project between	the prime	ereby agree that u Contractor and Conted above.			
M	BE/WBE	1 -		Prime Prop)ser	<u>.</u> .	
G&V Construction	on Certino	17		S Mechanic	al, (Rc)		11
Name of Firm	12. VI		الم	. // Name o		Maril	
By: C	an ju	<i>IT</i>	Vov	By: Signature	V J POU	W/M	
Anna Fayuzzi				Dave Amac			
Print Name				Print Ni	iné		
President Title		,,		Project Mai Title	nager	the state of the s	
1/24/2018			**************************************	1/24/2018		·	 ; 4.
Date				Date			

STATE OF	~_		STATE OF IL		
COUNTY OF	was		COUNTY OF Cook		
SUBSCRIBED AND SWORN	O before me on the	· · · · · · · · · · · · · · · · · · ·	SUBSCRIBED AND SWORN TO bef	fore me on the	
		2010			
24th day of Januar	, ZO	2018 .	24th day of January	, 20 2018 .	
Hinde	JOHN V		- Jan K		
Notary Public	11	· ·	Notary Public		
Reinted Name of Notes	thetw	Con	Janice K	eating h	
OFFICIAL SEAL	\$		·		····
LINDA HUFFMAN	AS REQUIRED BY INSTU F ILLINOIS & BID HEREV S 7/1/2021 &	ICTION TO BIDDER O WITH SUBMITTED - N	F/AND IN CONJUNCTION WITH OT REQUIRED	S OFFICIAL SE/	
ARV PUBLIC, STATE C	c 7/1/2021 2		-	JANICE KEATI	
TO: COUNTY OF STATE VEHICLE	O 11 (1944) 7 2		•	NOTARY PUBLIC - STATE	יווויייון זיט
COMMISSION	allin .		•	NOTARY PUBLIC - STATE MY COMMISSION EXPIR	
BID FOR:			- "		
BID FOR: BID DOCUMENT NUMBER:		BID	OPENING DATE:		
BID FOR: BID DOCUMENT NUMBER:	onditions of said proposal) the	BID	OPENING DATE:		
BID FOR: BID DOCUMENT NUMBER:		BID	OPENING DATE:		
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all c	onditions of said proposal) the	BID e following described d	OPENING DATE: eposit check:	MY COMMISSION EXPIR	
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all c	onditions of said proposal) the	BID e following described d () Other	OPENING DATE:	MY COMMISSION EXPIR	
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all c	onditions of said proposal) the	BID e following described d () Other	OPENING DATE: eposit check:	MY COMMISSION EXPIR	
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all c () Cashiers Check Drawn on:	onditions of said proposal) the	BID e following described d () Other of:	OPENING DATE: eposit check:	MY COMMISSION EXPIR	
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all c () Cashiers Check Drawn on: Draft or Check Number:	onditions of said proposal) the	BID e following described d () Other of:	OPENING DATE: eposit check:	MY COMMISSION EXPIR	
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all of the control of the	onditions of said proposal) the	BID e following described d () Other of:	OPENING DATE: eposit check:	MY COMMISSION EXPIR	
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all of the control of the	onditions of said proposal) the	BIDDER'S NAME	OPENING DATE: eposit check:	MY COMMISSION EXPIR	
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all of the control of the	onditions of said proposal) the	BID e following described d () Other of:	OPENING DATE: eposit check:	MY COMMISSION EXPIR	
BID FOR: BID DOCUMENT NUMBER: We deposit (subject to all of the control of the	onditions of said proposal) the	BIDDER'S NAME	OPENING DATE: eposit check:	MY COMMISSION EXPIR	

210

SECTION 7 - EXHIBITS

May 2015

EXHIBIT 1 - SUBCONTRACTOR'S CERTIFICATION CONCERNEING LABOR STANDARDS AND PREVAILING WAGE REQUIREMENTS

				- 1 -		
To t	(Contractor):			Date: 1/24/	2018	
	S Mechanic	al, Inc.		·		
	16420 S Kill	bourn Avenue		Project Numb	per:	D42132.00
	Oak Forest,	IL 60452			/4	The state of the s
				Project Name		all Floor Drains-Penthouse nent Rooms
1.	The underston	ed, having executed a Contract with		E Mark	anical, inc.	
·	tite miorialdu	in in a single over in section of initial states and the	14-4-4		tractor)	
				1		
	***	for	rCo	ncrete Work		(Nature of work)
			_in the amount of \$	80,782,00		
	In the construc	tion of the above-identified priect, certifies	that:			
	(a)	The Labor Standards provisions fo the Co aforesaid Contract.	intract for Constructio	n are included	in the	
	(b)	Neither he nor any firm, corporation, par substantial interest is designated as an ir General of the United States pursuant to Secretary of Labor, Part 5 (29 CFG, Part 5 Bacon Act, as amended [40 W.S.C. 276a-	eligible Contractor by Section 5.6(b) of the) or pursuant to Section	the Comptrol Regulations of	ler the	
	(c)	No part of the aforementioned Contract Subcontractor if such Subcontractor or a which such Subcontractor has a substant Contractor pursuant to any the aforesaid	ny firm, corporation, p ial interest is designat	oartnership or ed as an inelig	association	ia
2.	days after	to obtain and forward to the Contractor, fo the execution of any lower subcontract a S idends and Prevailing Wage Requirements,	lubcontractor's Certifi	cation Concern	าไทย	
3.	The works	nen will report for duty on or about	3/5/201	8	(date)	

SUBCONTRACTOR:

G&V Construction Co Inc

SIGNATURE;

DATE: 1/24/2018



TONI PRECKWINKLE

PRESIDENT

Cook County Board

of Commissioners

RICHARD R. BOYKIN

1st District

ROBERT STEELE 2nd District

JERRY BUTLER 3rd District

STANLEY MOORE 4th District

DEBORAH SIMS 5th District

EDWARD M, MOODY 6th District

JESUS G. GARCIA 7th District

LUIS ARROYO, JR. 8th District

PETER N. SILVESTRI 9th District

BRIDGET GAINER 10th District

JOHN P. DALEY 11th District

JOHN A. FRITCHEY 12th District

LARRY SUFFREDIN 13th District

GREGG GOSLIN 14th District

TIMOTHY O. SCHNEIDER 15th District

JEFFREY R. TOBOLSKI 16th District

SEAN M. MORRISON 17th District OFFICE OF CONTRACT COMPLIANCE

JACQUELINE GOMEZ

DIRECTOR

118 N. Clark, County Building, Room 1020 ● Chicago, Illinois 60602 ● (312) 603-5502

June 20, 2017

Ms. Anna Favuzzi, President G & V Construction Co., Inc. 5239 West Diversey Avenue Suite 201 Chicago, IL 60639

Re: Annual Certification Expires: June 20, 2018

Dear Ms. Favuzzi:

Congratulations on your continued eligibility for Certification as a **Women-owned Business Enterprise (WBE)** by Cook County Government. This certification is valid until **June 20, 2020**; however, you must re-validate your firms' certification annually.

As a condition of continued Certification, you must file a "No Change Affidavit" within sixty (60) business days prior to the date of Annual Certification Expiration. Failure to file this Affidavit shall result in the termination of your Certification. You must notify Cook County Government's Office of Contract Compliance of any change in ownership or control or any other matters or facts affecting your firm's eligibility for Certification within fifteen (15) business days of such change.

Cook County Government may commence action to remove your firm as a **WBE** vendor if you fail to notify us of any changes of facts affecting your firm's Certification, or if your firm otherwise fails to cooperate with the County in any inquiry or investigation. Removal of status may also be commenced if your firm is found to be involved in bidding or contractual irregularities.

Your firm's name will be listed in Cook County's Directory of certified firms in the following area(s) of specialty:

CONSTRUCTION: HIGHWAY, STREET, AND BRIDGE CONSTRUCTION; WATER, SEWER LINE AND RELATED STRUCTURES

Your firm's participation on Cook County contracts will be credited toward **WBE** goals in your area(s) of specialty. While your participation on Cook County contracts is not limited to your specialty, credit toward **WBE** goals will be given only for work performed in the specialty category.

Thank you for your continued interest in Cook County Government's Minority, Women, Veteran, and Service-Disabled Veteran Business Enterprise Programs.

Sincerely,

Jacqueline Gomez

Contract Compliance Director

JG/ew

Vendor Information



Vendor Information

Business Name

G & V CONSTRUCTION CO INC.

Owner

Ms. Anna Favuzzi

Address

5239 W. Diversey Ave.

> Mao This Address

Suite 201 Chicago, IL 60639

Phone

630-595-6474

Fax

Email

630-595-6477 anna@gvconstructionco.com

Certification information

Certifying Agency

Cook County

Certification Type

WBE - Women Business Enterprise

Certification Date

6/20/2017

Renewal Date

6/20/2018

Expiration Date

6/20/2020

Cartified Business

Construction: Highway, Street, and Bridge Construction; Water,

Description

Sewer Line and Related Structures

Commodity Codes

Code

Description

NAICS 23711

Water and Sewer Line and Related Structures Construction

NAICS 237110

Construction management, water and sewer line

NAICS 237110

Water and Sewer Line and Related Structures Construction

NAICS 237310

Bridge construction

NAICS 237310

Concrete paving (i.e., highway, road, street, public sidewalk)

NAICS 237310

Construction management, highway, road, street and bridge

NAICS 237310

Highway construction

Additional Information

Customer Support

Copyright @ 2018 B2Gnow. All rights reserved.

Print This Page

Vendor Information

CLOSE WINDOW X

Buelness Name

G & V CONSTRUCTION CO INC

Owner Address > Man This Address

Me. Anne Favuzzi 5239 W. Diversey Ave. Suite 201 Chicago, IL 60839

Phone

630 595 6474

830-595-6477

Email

anna@cyconstruction.co.com

Certification Information

Certifying Agency

Cook County

Certification Type Certification Date WBE - Women Business Enterprise 6/20/2017

Renewal Date

6/20/2018 6/20/2020

Explication Date

Construction: Highway, Street, and Bridge Construction; Water, Sewar Line and Related Structures

Carlified Business Description

Commodity Codes

Code

Description

NAICS 23711 NAICS 237110

Water and Sewar Line and Related Structures Construction Construction transgement, water and sewer line

NAICS 287110

Water and Sawer Line and Related Structures Construction

NAICS 237310

Bridge construction

NAICS 237310

Concrete paving (i.e., highway, road, street, public sidewalk)

NAICS 237310

Construction management, highway, road, street and bridge

NAICS 237310

Highway construction

Additional Information

Capyright @ 2018 82Gnow. All rights reserved.

Print This Page

this 24th day of January , 20 2018

Notary Public AMO WISZO WOOTY

SEAL

OFFICIAL SEAL
ANNA WISZOWATY
NOTARY PUBLIC - STATE OF ILLINOIS
MY COMMISSION EXPIRES: 11/16/2011

this 24th day of Jan

Notary Public

SEAL

Janice Keating

OFFICIAL SEAL

JANICE KEATING
NOTARY PUBLIC - STATE OF ILLINOIS
MY COMMISSION EXPIRES:03/31/20

May 2015

200

EXHIBIT G - LETTER OF INTENT BETWEEN PRIME CONTRACTOR AND MBE/WBE SUBCONTRACTOR OR SUPPLIER

COOK COUNTY, ILLINOIS LETTER OF INTENT BETWEEN PRIME CONTRACTOR AND MBE/WBE SUBCONTRACTOR OR SUPPLIER

Contract Title	CCB Install Floor Di Rooms	ains-Penthouse	& Equipme	contract Number:	042132.00	i	· · · · · · · · · · · · · · · · · · ·
Prime proposer:	S Mechan	ical, Inc.				<u></u>	·····
Address	16420 S Kilbourn /	Ave.			Oak Forest	<u>t</u>	60452
Telephone:	708-535-3600		FAX:	708-535-6655	City e mail: d	State amacher@smechanical.com	Zīp Code
Proposed Contra	act amount \$: 354	,618.16					
Proposed subcor	ntract amount: \$:	15,000.00		······································			
Type of agreeme	ent; <u>X</u>	lump sum	,	hourly rate	unit price		•
MBE/WBE subco	ontractor or supplier:	JM Polcurt,	inc.				····
Address 30	24 \$. 25th Avenue		_;		Broadview	<u>1L</u>	60155
Telephone:	Street 708-450-1	1156	FAX	John Marquez	City e mail:	State John@jmpolcurr	Zip Code .com
Work to be perfo	ormed by MBE/WBE:						
Power and Contr	rol Work						
fort		roject between	the prime	hereby agree that upon the Contractor and Cook Cour ated above.			
MI	BE/WBE			Prime Proposer			
IM Polcurr, Inc.	,	/	· · · · · · · · · · · · · · · · · · ·	S Mechanical, Inc	<u> </u>	M	/7_
Name of Firm	Mest	<u> </u>		Name of Firm	m	[[mh	lez
Signature	1			Signature	· · ·		,
John Marquez Print Name				Dave Amacher Print Name		The state of the s	
President Title	······································			Project Manager	· · · · · · · · · · · · · · · · · · ·		
1/24/2018				,	•		
1/24/2018 Date	 		.,	1/24/2018 Date		· · · · · · · · · · · · · · · · · · ·	

STATE OF IL COUNTY OF COOK SUBSCRIBED AND SWORN TO before me on the 24th day of January , 20 2018 . 24th day of January Notary Public STATE OF LUNOIS Printed Name of Notary NOTARY PUBLIC STATE OF LUNOIS TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID DOCUMENT NUMBER: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check () Bank Draft () Other Drawn on: BANK CITY Draft or Check Number: Date: Amount: \$ SUBSCRIBED AND SWORN TO LEDOK Notary Public January Notary Public January Notary Public January Notary Public Notary Pub	
SUBSCRIBED AND SWORN TO before me on the 24th day of January ,20 2018 . 24th day of January Notary Public	
SUBSCRIBED AND SWORN TO before me on the 24th day of January ,20 2018 . 24th day of January AMMA WISCOSTA . 24th day of January Printed Name of Notary Notary Public . 24th Deficiency Printed Name of Notary Y COMMISSION EXPIRES:11/19/20, STROUIRED BY INSTUCTION TO BIDDER OF/AND IN CONJUNICTION WITH BID HEREWITH SUBMITTED - NOT REQUIRED TO: Country of Cook BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check:) Cashiers Check () Bank Draft () Other Drawn on: Of: BANK CITY Draft or Check Number: Date: Amount: \$ SUBSCRIBED AND SWORN TO DE SUBMINARY BID DOCUMENT NOTARY Public . 24th day of January Printed Name of Notary BID DOCHMING NOTARY Public . 24th day of January Notary Public . 24th day of January Printed Name of Notary BID OPENING DATE: Date: Amount: \$ SUBMINITED - NOT WRITE IN THE SPACES BELOW	
24th day of January , 20 2018 . 24th day of January AMMA WISCOSOFY Notary Public Danic Printed Name of Notary Janic Printed Name of Notary COMMISSION EXPIRES: 11/16/20 S REQUIRED BY INSTUCTION TO BIDDER OF/AND IN CONJUNCTION WISBID HEREWITH SUBMITTED - NOT REQUIRED TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check () Bank Draft () Other Drawn on: BANK CITY Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	
Notary Public OFFICIAL SEALUNG AND THE Printed Name of Notary TARY PUBLIC - STAFE OFFICIANOS Y COMMISSION EXPIRES:11/16/20s REQUIRED BY INSTUCTION TO BIDDER OF/AND IN COMJUNCTION WITH BID HEREWITH SUBMITTED - NOT REQUIRED TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check () Bank Draft () Other Drawn on: BANK CITY Draft or Check Number: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	before me on the
TARY PUBLIC STATE OF ILLINOIS Y COMMISSION EXPIRES: 11/16/20 SERQUIRED BY INSTUCTION TO BIDDER OF/AND IN CONJUNCTION WITH BID HEREWITH SUBMITTED - NOT REQUIRED TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check BANK Drawn on: BANK Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	, 20 2018
TARY PUBLIC STATE OF ILLINOIS Y COMMISSION EXPIRES: 11/16/20 SERQUIRED BY INSTUCTION TO BIDDER OF/AND IN CONJUNCTION WITH BID HEREWITH SUBMITTED - NOT REQUIRED TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check BANK Drawn on: BANK Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	1
TARY PUBLIC STATE OF ILLINOIS Y COMMISSION EXPIRES: 11/16/20 SERQUIRED BY INSTUCTION TO BIDDER OF/AND IN CONJUNCTION WITH BID HEREWITH SUBMITTED - NOT REQUIRED TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check BANK Drawn on: BANK Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	- Car
TARY PUBLIC STATE OF ILLINOIS Y COMMISSION EXPIRES: 11/19/20 REQUIRED BY INSTUCTION TO BIDDER OF/AND IN CONJUNCTION WITH BID HEREWITH SUBMITTED - NOT REQUIRED TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check Bank Draft Other Drawn on: BANK CITY Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	ce Keating
Y COMMISSION EXPIRES:11/16/20 REQUIRED BY INSTUCTION TO BIDDER OF/AND IN CONJUNCTION WITH BID HEREWITH SUBMITTED - NOT REQUIRED TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check () Bank Draft () Other Drawn on: BANK CITY Draft or Check Number: Arnount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	**************************************
TO: County of Cook BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check () Bank Draft () Other Drawn on: BANK CITY Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	OFFICIAL S
BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check () Bank Draft () Other Drawn on: BANK CITY Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	S NOTARY PUBLIC STAT
BID FOR: BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check () Bank Draft () Other Drawn on: BANK CITY Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	MY COMMISSION EXP
BID DOCUMENT NUMBER: BID OPENING DATE: We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check () Bank Draft () Other Drawn on: BANK CITY Draft or Check Number: Date: Amount: \$ Submitted by: BIDDER'S NAME CITY STATE DO NOT WRITE IN THE SPACES BELOW	•
We deposit (subject to all conditions of said proposal) the following described deposit check: Cashiers Check Bank Draft Other	. .
Drawn on: BANK Of: BANK CITY Draft or Check Number: Amount: \$ Submitted by: BIDDER'S NAME CITY STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	
Drawn on: BANK Of: BANK CITY Draft or Check Number: Amount: \$ Submitted by: BIDDER'S NAME CITY STREET ADDRESS CITY DO NOT WRITE IN THE SPACES BELOW	
Drawn on: BANK CITY Draft or Check Number: Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	
BANK CITY Draft or Check Number:	
Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	STATE
Amount: \$ Submitted by: BIDDER'S NAME STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	
Submitted by: BIDDER'S NAME STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	·· ·
STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	
STREET ADDRESS CITY STATE DO NOT WRITE IN THE SPACES BELOW	
CITY STATE DO NOT WRITE IN THE SPACES BELOW	
CITY STATE DO NOT WRITE IN THE SPACES BELOW	· · · · · · · · · · · · · · · · · · ·
DO NOT WRITE IN THE SPACES BELOW	
	ZIP CODE
The Above Described Deposit Check is:	
·	

EXHIBIT I - SUBCONTRACTOR'S CERTIFICATION CONCERNEING LABOR STANDARDS AND PREVAILING WAGE REQUIREMENTS

Τσ	(Contractor):			Date: 1/24/20	18
	\$ Mechanical, Inc. 16420 S Kilbourn Avenue Oak Forest, IL 60452			Project Number	r: 042132.00
•				CCB Inst Project Name: <u>Equipme</u>	
1.	The undersign	ed, having executed a Contract with		ical, Inc.	
		fo	Po <u>wer</u>	and Control Worl	(Nature of work)
			in the amount of \$	15,000.00	
	in the construction (a)	The Labor Standards provisions fo the Colaforesaid Contract. Neither he nor any firm, corporation, part substantial interest is designated as an in-	ntract for Construction	n in which he has	
		General of the United States pursuant to Secretary of Labor, Part 5 (29 CFG, Part 5) Bacon Act, as amended [40 W.S.C. 276a-2	Section 5.6(b) of the F For pursuant to Section	Regulations of the	
	(c)	No part of the aforementioned Contract I Subcontractor if such Subcontractor or an which such Subcontractor has a substanti Contractor pursuant to any the aforesaid	y firm, corporation, p al interest is designate	artnership or asso ed as an ineligible	ociation in
2.	days after	to obtain and forward to the Contractor, for the execution of any lower subcontract a Su dards and Prevailing Wage Requirements, e	bcontractor's Certific	ation Concerning	
3.	The workn	nen will report for duty on or about	3/5/201	18	(date)

	es that:		
(a)	the legal name and the busines.	s address of the undersigned are:	
	JM Polcurr, Inc. 3024 S. 25th Avenue Broadview IL	60155	·
(b)	The undersigned is (check one):		
	Sole Proprietorship		
	X Parnership Corporation Other Organization	on (Describe) 0	
(c)	The Name and address of the o	wner partners or officers	
(0)	of the undersigned are:		
(4)	of the undersigned are: Name	Title	ADDRESS
(c)		Title President	ADDRESS 1903 E. Illinois Street, Wheaton, IL 50187
(~)	Name		
(~)	Name John Marquez	President	1903 E. Illinois Street, Wheaton, IL 60187

SUBCONTRACTOR;

JM Polcurr, Inc.

SIGNATURE:

DATE: 1/24/2018



AUG - 8 2014

DEPARTMENT OF PROCUREMENT SERVICES CITY OF CHICAGO

John Marquez
JM Polcurr, Inc.
10127 W. Roosevelt Rd
Westchester, IL 60154

Dear John Marquez:

We are pleased to inform you that JM Polcurr, Inc. has been recertified as a Minority-Owned Business Enterprise ("MBE") by the City of Chicago ("City"). This MBE certification is valid until 8/1/2019; however your firm's certification must be revalidated annually. In the past the City has provided you with an annual letter confirming your certification; such letters will no longer be issued. As a consequence, we require you to be even more diligent in filing your annual No-Change Affidavit 60 days before your annual anniversary date.

It is now your responsibility to check the City's certification directory and verify your certification status. As a condition of continued certification during the five year period stated above, you must file an annual No-Change Affidavit. Your firm's annual No-Change Affidavit is due by 8/1/2015, 8/1/2016, 8/1/2017, and 8/1/2018. Please remember, you have an affirmative duty to file your No-Change Affidavit 60 days prior to the date of expiration. Failure to file your annual No-Change Affidavit may result in the suspension or rescission of your certification.

Your firm's five year certification will expire on 8/1/2019. You have an affirmative duty to file for recertification 60 days prior to the date of the five year anniversary date. Therefore, you must file for recertification by 6/1/2019.

It is important to note that you also have an ongoing affirmative duty to notify the City of any changes in ownership or control of your firm, or any other fact affecting your firm's eligibility for certification within 10 days of such change. These changes may include but are not limited to a change of address, change of business structure, change in ownership or ownership structure, change of business operations, gross receipts and or personal net worth that exceed the program threshold. Failure to provide the City with timely notice of such changes may result in the suspension or rescission of your certification. In addition, you may be liable for civil penalties under Chapter 1-22, "False Claims", of the Municipal Code of Chicago.

Please note – you shall be deemed to have had your certification lapse and will be ineligible to participate as a **MBE** if you fail to:

- File your annual No-Change Affidavit within the required time period;
- Provide financial or other records requested pursuant to an audit within the required time period;
- Notify the City of any changes affecting your firm's certification within 10 days of such change; or
- File your recertification within the required time period.

Please be reminded of your contractual obligation to cooperate with the City with respect to any reviews, audits or investigation of its contracts and affirmative action programs. We strongly encourage you to assist us in maintaining the integrity of our programs by reporting instances or suspicions of fraud or abuse to the City's Inspector General at chicagoinspectorgeneral.org, or 866-IG-TIPLINE (866-448-4754).

Be advised that if you or your firm is found to be involved in certification, bidding and/or contractual fraud or abuse, the City will pursue decertification and debarment. In addition to any other penalty imposed by law, any person who knowingly obtains, or knowingly assists another in obtaining a contract with the City by falsely representing the individual or entity, or the individual or entity assisted is guilty of a misdemeanor, punishable by incarceration in the county jail for a period not to exceed six months, or a fine of not less than \$5,000 and not more than \$10,000 or both.

Your firm's name will be listed in the City's Directory of Minority and Women-Owned Business Enterprises in the specialty area(s) of:

NAICS Code(s):

238210 - Electrical Contractors

Your firm's participation on City contracts will be credited only toward **Minority-Owned Business Enterprise** goals in your area(s) specialty. While your participation on City contracts is not limited to your area of specialty, credit toward goals will be given only for work that is self-performed and providing a commercially useful function that is done in the approved specialty category.

Thank you for your interest in the City's Minority and Women-Owned Business Enterprise (MBE/WBE) Program.

Sincerely,

Jamie L. Rhee

Chief Procurement Officer

JLR/gd

Vendor Information

CLOSE WINDOW

Vendor Information

Business Name

JM Polcurr, Inc., DBA n/a

Owner

Mr. John Marquez

Address

3024 S. 25th Avenue Broadview, IL 60155

> Mao This Address

708-450-1156

Phone Fax

708-450-1157

Email

john@impolcurr.com

Website

www.impoleurrine.com

Certification Information

Certifying Agency

City of Chicago

Certification Type

MBE - Minority Business Enterprise

Certification Date

8/3/2017

Renewal Date

8/1/2018

Expiration Date

8/1/2019

Certified Business Description

NAICS 238210 Electrical contractors NAICS 237130 Alternative Energy; Solar Power Structure

Construction; Fiber Optic Cable Transmission Line Construction; Underground Cable (Cable TV, electricity, telephone laying); Utility line (communications, electric power) Construction

Commodity Codes

Code

Description

NAICS 237130

Atternative energy (e.g., geothermal, ocean wave, solar, wind) structure

construction

NAICS 237130

Fiber optic cable transmission line construction

NAICS 237130

Solar power structure construction

NAICS 237130

Underground cable (e.g., cable television, electricity, telephone) laying

NAICS 237130

Utility line (i.e., communication, electric power), construction

NAICS 238210

Electrical contractors

Additional Information

Customer Support

Print This Page

Copyright @ 2018 B2Gnow. All rights reserved.

Vendor Information

GLOSE VANDOVI (X)

Vendor Information

Address > Map 7his Address

Business Name Owner

JM Poleure, Inc., DBA n/a Mr. John Marques 3024 S. 25th Avenus Broadylew, IL 60155

Phone Fax Email

708-450-1157 iohn@impolcum.com www.impoleumine.com

Certification information

Cerlifying Agency

City of Chicago

708-450-1156

Cartification Type

MBE - Minurity Business Enterprise

Certification Data Renewal Date Expiration Data

8/3/2017 8/1/2018 8/1/2019

Certified Business Description

NAICS 238210 Electrical contractors
NAICS 237130 Alternative Energy; Solar Power Structure
Construction; Filer Optic Cable Transmission Line Construc
Underground Cable (Cable Ty, electricity, talephone saying);
Utility Ilns (communications, electric power) Construction

Commodity Codes

Cescription Code

Alternative energy (e.g., geothermal, ocean wave, solar, wind) structure construction NAICS 237130

NAICS 237130 Fiber optic cable transmission line construction

Solar power structure construction

Underground cable (e.g., cable television, electricity, telephone) laying NAICS 237130

Utility line (f.e., communication, electric power), construction NAICS 23713D

NAICS 238210 Electrical contractors

Additional Information

Print This Page

Curtomer Support
Copyright © 2018 B2Gnow. All rights reserved.

Cook County Office of the Chief Procurement Officer Identification of Subcontractor/Supplier/Subconsultant Form

OCPO ONLY	
O Disqualification	
Check Complete	

The Bidder/Proposer/Respondent ("the Contractor") will fully complete and execute and submit an identification of Subcontractor/Supplier/Subconsultant Form ("ISF") with each Bid, Request for Proposal, and Request for Qualification. The Contractor must complete the ISF for each Subcontractor, Supplier or Subconsulant which shall be used on the Contract, in the event that there are any changes in the utilization of Subcontractors, Suppliers or Subconsultants, the Contractor must file an updated ISF.

Bid/RFP/RFQ No:	1555-14475-M	IQ5	Date:	1/24/2018	
Total Bid or Proposal A	mount: \$354,61	3.16	Contract Title:	CCB Install Floor	Drains-Penthouse &
Contractor:	S Mechanical, In		Subcontractor/Supplier/ Subconsultant to be added or substitute	J.M.Polcurr	
Authorized Contact for Contractor	Dave Amacher		Authorized Contact for Subcontractor/Supplier/ Subconsultant	John Marquez	
Email Address (Contractor)	damacher@sme	chanical.com	Email Address (Subcontractor)	john@impolcur	r.com
Company Address (Contractor)	16420 \$ Kilbour	ń	Company Address (Subcontractor)	3024 \$ 25th Ave	inu d
City, State and Zip (Contractor)	Oak Forest, IL 6	0452	City, State and Zip (Subcontractor)	Broadview, IL 60	0155
Telephone and Fax (Contractor)	708-535-3600 708-533-6655 F		Telephone and Fax (Subcontractor)	708-450-116 708-450-1157	
Estimated Start and Completion Dates (Contractor)	Start: Completion:	3/5/2018 7/5/2018	Estimated Start and Completion Dates (Subcontractor)	Start: Completion:	3/5/2018 7/5/2018

Note: Upon request, a copy of all written subcontractor agreements must be provided to the OCPO.

	Total Price of
Description of Services or Supplies	<u>Subcontract for</u>
	Services or Supplies
Power and control work	\$15,000.00

The subcontract documents will incorporate all requirements of the Contract awarded to the Contractor as applicable. The subcontract will in no way hinder the Subcontractor/Supplier/Subconsultant from maintaining its progress on any other contract on which it is either a Subcontractor/Supplier/Subconsultant or principal contractor. This disclosure is made with the understanding that the Contractor is not under any circumstances relieved of its abilities and obligations, and is responsible for the organization, performance, and quality of work. This form does not approve any proposed changes, revisions or modifications to the contract approved MSE/WBE Utilization Plan. Any changes to the contract's approved MSE/WBE/Utilization Plan must be submitted to the e Office of the Contract Compilance.

Contractor	
S Mechanical, Inc.	
Name Project Manage	
Title Jove ///m/m	1/24/2018
Prime Contractor Signature	Date

May 2015

Cook County Office of the Chief Procurement Officer Identification of Subcontractor/Supplier/Subconsultant Form

	OCPO ONLY	-
0	Disqualification	
0	Check Complete	

The Bidder/Proposer/Respondent ("the Contractor") will fully complete and execute and submit an identification of Subcontractor/Supplier/Subconsultant Form ("ISF") with each Bid, Request for Proposal, and Request for Qualification. The Contractor must complete the ISF for each Subcontractor, Supplier or Subconsulant which shall be used on the Contract. In the event that there are any changes in the utilization of Subcontractors, Suppliers or Subconsultants, the Contractor must file an updated ISF.

Bid/RFP/RFQ No:	1565-1447	75-MC5	Date:	1/24/2018		
Total Bid or Proposal	Amount: \$354,618.	16	Contract Title:	CCB install Floor Drains-Penthouse		
Contractor:	S Mechanical, Inc		Subcontractor/Supplier/ Subconsultant to be added or substitute	G&V Construction Co. Inc.		
Authorized Contact Dave Amacher for Contractor			Authorized Contact for Subcontractor/Supplier/ Subconsultant	Anna Favuzzi		
Email Address (Contractor)	damacher@smechanical.com		Email Address (Subcontractor)	anna@gvconstructionco.com		
Company Address (Contractor)	16420 S Kilbourn		Company Address (Subcontractor)	5239 W Diversey Ave, Suite 201		
City, State and Zip (Contractor)	Oak Forest, IL 60452		City, State and Zip (Subcontractor)	Chicago, IL 60639		
Telephone and Fax (Contractor)	708-535-3600 708-535-6655 F		Telephone and Fax (Subcontractor)	630-595-6474 630-595-6477		
Estimated Start and Completion Dates (Contractor)	Start: Completion:	3/5/2018 7/5/2018	Estimated Start and Completion Dates (Subcontractor)	Start; Completion:	3/5/2018 7/5/2018	

Note: Upon request, a copy of all written subcontractor agreements must be provided to the OCPO.

Description of Services or Supplies	Total Price of Subcontract for Services or Supplies
Concrete Work	\$80,782.00

Contractor	
Mechanical, Inc.	
Name Project Manager	
Title / m /////////////////////////////////	4 to 4 to 200
Prime Contractor Signature	1/24/2018 Date

Cook County Office of the Chief Procurement Officer Identification of Subcontractor/Supplier/Subconsultant Form

Ì	OCPO ONLY
ł	O Disqualification
ł	Check Complete

The Bidder/Proposer/Respondent ("the Contractor") will fully complete and execute and submit an identification of Subcontractor/Supplier/Subconsultant Form ("iSF") with each Bid, Request for Proposal, and Request for Qualification. The Contractor must complete the ISF for each Subcontractor, Supplier or Subconsulant which shall be used on the Contract. In the event that there are any changes in the utilization of Subcontractors, Suppliers or Subconsultants, the Contractor must file an updated ISF.

Bid/RFP/RFQ No:	1555-14475-MC5		Date:	1/24/2018			
Total Bid or Proposa	Amount: \$354,61	8,16	Contract Title:	CCB Install Floor D & Equipment Root			
Contractor:	S Mechanical, Inc		Subcontractor/Supplier/ Subconsultant to be added or substitute	J.S.R. Enterprises, Inc.			
Authorized Contact Dave Amacher for Contractor		Authorized Contact for Subcontractor/Supplier/ Subconsultant	Jerry Roberts				
Email Address (Contractor)	damacher@smechanical.com		Email Address (Subcontractor)	sroberts@isrent.com			
Company Address Contractor	16420 S Klibaurn		Company Address (Subcontractor)	4931 W 173rd St. Unit D			
City, State and Zip (Contractor)	Oak Forest, IL 60452		City, State and Zip (Subcontractor)	Country Club Hills, IL 60478			
Telephone and Fax Contractor)	708-535-3600 708-535-6655 F		sample del		Telephone and Fax (Subcontractor)	708-206-1800 708-206-1879	
Estimated Start and Completion Dates (Contractor)	Start: Completion:	3/5/2018 7/5/2018	Estimated Start and Completion Dates (Subcontractor)	Start:	3/5/2018 7/5/2018		

Note: Upon request, a copy of all written subcontractor agreements must be provided to the OCPO.

Description of Services or Supplies	Total Price of Subcontract for Services or Supplies
Plumbing Work	\$25,000.00

Contractor		
S Mechanical, inc.	•	
Name Project Manager		
Title / Me / //////////////////////////////	1/24/2018	
Printe Contractor Signature	Date	

RESPONSIBLE BIDDER REQUIREMENT

In accordance with the provisions of Section 30-22 (6) of the Illinois Procurement Code, the bidder certifies that it is a participant, either as an individual or as part of a group program, in the approved apprenticeship and training programs applicable to each type of work or craft that the bidder will perform with its own forces. The bidder further certifies for work that will be performed by subcontract that each of its subcontractors. submitted for approved either (a) is, at the time of such bid, participating in an approved, applicable apprenticeship and training program; or (b) will, prior to commencement of performance of work pursuant to this centered, begin participation in an approved apprenticeship and training program applicable to the work of the subcontract. The Department, at any time before or after award, may require the production of a copy of each applicable Certificate of Registration Issued by the United States Department of Labor evidencing such participation by the contractor and any or all of its Subcontractors. Applicable apprenticeship and training programs are those that have been approved and registered with the United States Department of Labor. The bidder shell list in the space below, the official name of the program sponsor holding the Certificate of Registration for all of the types of work or crafts in which the bidder is a participant and that will be performed with the bidder's forces. Types of work or craft work that will be subcontracted shall be included and listed as subcontract work. The list shall also indicate any type of work or craft job category that does not have an applicable apprenticeship or training program. The bidder is responsible for making a complete report and shall make certain that each type of work or craft job category that will be utilized on the project is accounted for and listed.

Pipefitters Union 597		
Sheet Metal Workers 73		
150,502,701,786 Laborers		
Local Union 134		 . , , , , , , , , , , , , , , , , , , ,
Local 5,130,150		
	.,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	

The requirements of this certification and disclosure are a material part of the contract, and the contractor shall require this certification provision to be included in all approved subcontracts. In order to fulfill this requirement, it shell not be necessary that an applicable program sponsor be currently taking or that it will take applications for apprenticeship, training or employment during the performance of the work of this contract.

Intial Revie	wer:	Final Reviewer:			RFP / CONTRACT REVIEW				
Contract #:	н.	1555-14475-MC5		Projec	t Description:	tion: 2016 JOC PROGRAM			
Requisition	#:	10000042458							
* /endor Nan	ne:	S MECH	ANICAL,	INC.					
Department	t:	CAPITAL	PLANNI	NG AND POLICY	Depar	tment Contact:	SEAMEAH LLOYD		
	*								
Contract Ph	one:	1			Contra	act Email:	SEAMEAH.LLOYD@COC	KCOUNTYIL GC	<u> 2V</u>
Date Req. R	lec'd:	03/13/1	.8	Bid Opening:		· · · · · · · · · · · · · · · · · · ·	Board Approval:	Yes	No
Date to Buy		03/13/1		Pre-Bid Meeting:			Board Meeting:		
Date to Use				Recommendation	Letter Rec'o	l:	Item Number:		
Date Singe				Compliance Letter			Fact Sheet for CPC):	
Advertisem					···				
						· .			
Contract Te					Renev	wal Options:	YesNo	#	Years
Contract Ar	nount: \$	<u> </u>							
Date	Intials	1				Notes			
03/13/18	CJ	ASSIGN	FD AND I	GAVE TO LILLIAN.	· -				
3/14	(1)		L- 10			*			
	. 10	Regi	c 1	IST From	3 TEG	7			
3/14		100	sent	PO BHR	<i>.</i>			<u></u>	
3/28	1	100	mm	- 10 T	T io		./ (// //	<i>y</i> -	
1 43	- a-	le	- The		- to 1811	yer on o	rlas partipul te	- 185c	<u>e/</u>
1 -	A		SIV	leburel	Engur	200	1-~	<u></u>	
415	1	Plea	mne	il gran	TEG				
-415	(A)	20	man	w"	· ·				
45/18	<u>a</u>	Rec	- lei	Id about	who c	po			
				1					
46	-			·				, .	
.			•						
	*	<u> </u>		,					
		, .							· · · · · · · · · · · · · · · · · · ·
(p-									
			•						
<u> </u>		-							·
		ļ				· · · · · · · · · · · · · · · · · · ·		···	
L									
	<u> </u>		· · · · · ·	,					
	 								

•		
Date	Intials	Notes
-50		
	·-	
	7	
€.		
	*	
Re-		
· · · · · · · · · · · · · · · · · · ·		
· · · · · · · · · · · · · · · · · · ·		
	.	
x.		
÷		
	*	
72+		
:	9 .	

CCG (PL)		Printed Requisit	 13:3:
Report Param	eters	2/1	
Requisition Numbers F		3/14	į
CCG (PL)	To: 100000424		137
Requisition: 10000042458 Requisition Type: Purchase Requisiti Creation Date: 07-MAR-18 Description: Project ID: 23316 Note To Approver: Notes:		A The state of the	
Line Line Type Item	Rev Category	Description	oun
Need By	Source rgent Type	Source	
1 Goods LLOYD, SEAMEAH M	72120000 Supplier	JOC Wprk Order #042132.00 Amou 5372,349.07 10000042458	. 0.01
Distributions: .01 A Justification: Note To Approver; Notes: Attachment is not		ount: 11569.1031.1:vzz.sovius.00000.00000	Total; 0.0
Previous Approvals:	·		
Sequence Date Approver	Action	Note	
1 07-MAR-18 LLOYD, SEAMEAH M		Joc Package	
Approval Action (Circle One);			
Approve Forward Reject			
Forward To:			
Note:			

Carolynn Jones (Procurement)

From:

James Fitzpatrick (Procurement)

Sent:

Monday, March 12, 2018 4:52 PM

Tồ:

Carolynn Jones (Procurement); Jacqueline Taylor (Procurement)

Cc:

Alesia Hawkins (Procurement); Cho Ng (Procurement); Danuta Rusin (Procurement);

Lillian Lee (Procurement); Barbie Flock (Procurement)

Subject:

Req assignments for 3/13

Carolynn / Jacqueline,

Please complete the following req assignments:

- * 1. 10000038619 to Donna as a new contract using 1855-17209
 - 2. 10000041076 to Donna as a new contract using 1855-17275
 - 3. 10000042765 to Donna as a JOC W/O under 1555-14475-GC1
 - 4. 10000042457 to Lillian as a JOC W/O under 1555-14475-MC SBE16
 - 5. 10000042458 to Lillian as a JOC W/O under 1555-14475-MC5
 - 6. 10000042241 to Barbie as a new contract using 1884-17305

Thanks!

James Fitzpatrick Operations Analyst Office of the Chief Procurement Officer 118 N. Clark St – Room 1018 312.603.1490



Lillian Lee (Procurement)

From:

Freeman Banks <f.banks@gordian.com>

Sent:

Thursday, April 05, 2018 10:48 AM

To:

Lillian Lee (Procurement)

Subject:

RE: WO#42132 for CCB Install Floor Drains-Penthouse & Equipment Rooms

I'm stating that S. Mechanical Engineering will be assisting with advising and inspection services for S. Mechanical Construction Company. They have two companies in one organization.

Please contact me if you have any questions.

Respectfully,

Freeman A. Banks

Account Manager – Great Lakes Region, CHICAGO, ILLINOIS

GORDIAN® Building knowledge

a: 30 Patewood Drive, Suite 350, Greenville, SC 29615

m: 312.856.6141

w: www.gordian.com | w: www.rsmeans.com

From: Lillian Lee (Procurement) < lillian.lee@cookcountyil.gov>

Sent: Thursday, April 5, 2018 10:24 AM
To: Freeman Banks <f.banks@gordian.com>

Subject: RE: WO#42132 for CCB Install Floor Drains-Penthouse & Equipment Rooms

Hi Freeman,

Are you stating that S Mechanical Engineers will be assisting S. Mechanical Engineers as needed, to advise and inspect the installation for the above listed WO? Please advise.

Thanks Lillian

From: Freeman Banks [mailto:f.banks@gordian.com]

Sent: Wednesday, April 04, 2018 2:35 PM

To: Lillian Lee (Procurement)

Subject: RE: WO#42132 for CCB Install Floor Drains-Penthouse & Equipment Rooms

It's S. Mechanical Engineers. They have two separate operations, Construction and Engineering.

Please contact me if you have any questions.

Respectfully,

Freeman A. Banks

Account Manager – Great Lakes Region, CHICAGO, ILLINOIS

G@RDIAN°

Building knowledge

a: 30 Patewood Drive, Suite 350, Greenville, SC 29615

m: 312.856.6141

w: www.gordian.com | w: www.rsmeans.com

From: Lillian Lee (Procurement) < lillian.lee@cookcountyil.gov>

Sent: Wednesday, April 4, 2018 1:18 PM
To: Freeman Banks <f.banks@gordian.com>

Subject: RE: WO#42132 for CCB Install Floor Drains-Penthouse & Equipment Rooms

Hi

Can you provide the name of the company that will assist S. Mechanical with this WO?

Thanks, Lillian

From: Freeman Banks [mailto:f.banks@gordian.com]

Sent: Wednesday, April 04, 2018 1:10 PM

To: Lillian Lee (Procurement)

Subject: RE: WO#42132 for CCB Install Floor Drains-Penthouse & Equipment Rooms

Line item #7 is the Engineer assisting the contractor (S. Mechanical) with advising and inspecting.

Please contact me if you have any questions.

Respectfully,

Freeman A. Banks

Account Manager - Great Lakes Region, CHICAGO, ILLINOIS

G&RDIAN°

Building knowledge

a: 30 Patewood Drive, Suite 350, Greenville, SC 29615

m: 312.856.6141

w: www.gordian.com | w: www.rsmeans.com

From: Lillian Lee (Procurement) < lillian.lee@cookcountyil.gov>

Sent: Tuesday, April 3, 2018 3:20 PM

To: Freeman Banks < f.banks@gordian.com>

Subject: WO#42132 for CCB Install Floor Drains-Penthouse & Equipment Rooms

Hi Freemen,

As per our conversation please see the attached document.

Thanks, Lillian



TONI PRECKWINKLE

PRESIDENT

Cook County Board of Commissioners

RICHARD R. BOYKIN

1st District

DENNIS DEER 2nd District

JERRY BUTLER 3rd District

STANLEY MOORE
4th District

DEBORAH SIMS 5th District

EDWARD M. MOODY 6th District

JESUS G. GARCIA 7th District

LUIS ARROYO JR 8th District

PETER N. SILVESTRI 9th District

BRIDGET GAINER 10th District

JOHN P. DALEY 11th District

JOHN A. FRITCHEY 12th District

LARRY SUFFREDIN 13th District

GREGG GOSLIN 14th District

TIMOTHY O. SCHNEIDER

JEFFREY R. TOBOLSKI 16th District

SEAN M. MORRISON 17th District BUREAU OF HUMAN RESOURCES

VELISHA L. HADDOX

BUREAU CHIEF

118 North Clark Street, Room 840 ● Chicago, Illinois 60602 ● (312) 603-3300

TO:

COUPE member unions (See attached list)

VIA EMAIL

FROM:

BHR - Labor Relations

RE:

Notification Pursuant to Extension Agreement

DATE:

March 14, 2018

Pursuant to the Extension Agreement between the Coalition of Unionized Public Employees (COUPE) and the County of Cook, you are hereby notified that the County intends to undertake the following construction work:

CCB Install Floor Drains-Penthouse & Equipment Rooms

This work will be performed under the Job Order Contracting Agreement referenced above with **S Mechanical, Inc.** The General Contractor intends to use a subcontractor three (3) subcontractors for this project. The name and address of the contractor and subcontractor(s) are as follow:

GENERAL CONTRACTOR

S Mechanical, Inc. 16420 S Kilbourn Oak Forest, IL 60452

SUBCONTRACTORS

J.M. Polcurr 3024 s. 25TH Ave Broadview, IL 60155

G&V Construction Co. Inc. 5239 W. Diversely Ave. Suite 201 Chicago, IL 60639

J.S.R. Enterprises, Inc. 4931 W. 173rd St. Unit D Country Club Hills, IL 60478

Please contact Phyllis Woods, Labor Liaison Officer at 312-603-5290 if you have any questions or concerns. Procurement Awarded Contracts can be found at the following link: www.cookcountyil.gov/procurement.

Cc: Shannon Andrews, CPO
Margaret Angelucci
Michael Leyden

\$ Fiscal Responsibility ₹ Innovative Leadership ♠ Transparency & Accountability ๗ Improved Services

COUPE MEMBER UNIONS

First Name	Last Name	E-mail Address	Company
John	Valone	<u>ivalone@iuec2.com</u>	Elevator Constructors, Local 2
Don	Finn	dfinn134@gmail.com	Local 134, IBEW
Harrison	Mailey	hmailey@pf597.org	Pipefitters, Local 597
Thomas	Ryan, Jr.	tryanjr@carpentersunion.org	Carpenters
Joe	Healy	joeh@local1092.org	Local 1092
Joe	Rinehart	jrinehart265@yahoo.com	Painters
John	Manley	opcmia5@sbcglobal.net	Plasterers
John	Riel	jriel@boilermakersone.org	Boilermakers
John	Spiros	ba147@aol.com	830,27, & 14
Larry	McNiff	Larry.McNiff@iwlocal63.com	Ironworkers
Mark	O'Donnell	local830@aol.com	830
Michael	Tierney	mtierney@ualocal130.org	Plumbers
Mike	Lowery	MLOWERY@bacadc1.org	Bricklayers
Paul	Wende	paul.wende@iwlocal63.com	Ironworkers
Ramon	Williams	ramonw@teamsterslocal700.com	Teamsters 700
Ray	Suggs	raysuggs@aol.com	Sheet Metal Workers
Terry	O'Brien	tobrien@local150.org	Operating Engineers
Terry	Shannon	tvshannon46@yahoo.com	Bricklayers
Thomas	Gavin	tgavin@ualocal130.org	Plumbers
Bill	Mangin	local17bill@gmail.com	Insulators
Tom	Ryan	ubclocal13@aol.com	Carpenters
Ryan	Kelly	ryan.kelly@iamdistrict8.org	IAM, 8

U

BACKGROUND CHECKLIST

SUB-CONTRACTOR COMPLIANCE VERIFICATION

COOK COUNTY OFFICE OF THE CHIEF PROCUREMENT OFFICER

Vendor Name: JM Polcur
U Sole Source U Quotes U Reference Contract U Contract U RFP U RFQ No. 1555-1447
1. System for Award Management (S.A.W.): https://www.sam.gov/portal/public/SAM/
Date searched: 3 171 Results print-out attached
City of Chicago Debarred List: http://www.cityofchicago.org/city/en/depts/dos/piovdis/comp/sycs/debarred_firms_list.html
Date searched: 31416 Results print-out estached Vendor Warne: 6 11 Conduct - Ce Que 1
O sole Source O Quotes O Reference Contract O Contract O NEP O REGINO.
1. System for Award Menagement (SAM): https://www.sam.gov/portal/public/SAM/ Date searched: 3 14 8 Results print-out attached 2. City of Chlego Debarred List: http://www.cityofchicago.org/city/en/depts/eps/provdrs/comp/svcs/debarred firms list.html
Onte searched: 314 Results print-out attached Vendor Name: 45 Calumns Ove
I sole Source I Quotes I Reference Contract I Comract I RFP I RFQ No.
1. System for Award Management (SARM): https://www.sam.gov/portal/public/SAM/ Date searched: Results print-out attached 2. City of Chicago Debarred List:
City of Chicago Debarred List: http://www.cityofchicago.org/city/en/depts/dps/provdrs/comp/svcs/debarred-firms-list.html
Date searched: 3/14/18 Results print-out attached

Cook County Office of the Chief Procurement Officer Identification of Subcontractor/Supplier/Subconsultant Form

O	CPO ONLY
O Disqu	ualification
	k Complete

The Bidder/Proposer/Respondent ("the Contractor") will fully complete and execute and submit an identification of Subcontractor/Supplier/Subconsultant Form ("ISF") with each Bid, Request for Proposal, and Request for Qualification. The Contractor must complete the ISF for each Subcontractor, Supplier or Subconsulant which shall be used on the Contract. In the event that there are any changes in the utilization of Subcontractors, Suppliers or Subconsultants, the Contractor must file an updated ISF.

	1655-14475-MC	5	Date:	1/24/2018	
rid/RFP/RFQ No:			Contract Title:	CCB Install Floor	rains-Penthouse 8
otal Bid or Proposal A Contractor:	S Mechanical, Inc.	<u></u>	Subcontractor/Supplier/ Subconsultant to be added or substitute	J.M.Polcurr	
Authorized Contact	Dave Amacher		Authorized Contact for Subcontractor/Supplier/ Subconsultant	John Marquez	
for Contractor Email Address (Contractor)	damacher@smec	hanical.com	Email Address (Subcontractor)	jehn@impolcurr.	com
Company Address (Contractor)	15420 S Kilbourn		Company Address (Subcontractor)	3024 S 25th Ave	nue
City, State and Zip (Contractor)	Oak Forest, IL 60	1452	City, State and Zip (Subcontractor)	Broadview, IL 60	155
Telephone and Fax (Contractor)	708-535-3600 708-535-6655 F		Telephone and Fax (Subcontractor)	708-450-116 708-450-1157	
Estimated Start and Completion Dates (Contractor)	Start: Completion:	3/5/2018 7/5/2018	Estimated Start and Completion Dates (Subcontractor)	Start: Completion:	3/5/2018 7/5/2018

Note: Upon request, a copy of all written subcontractor agreements must be provided to the OCPO.

	Description of Services or Supplies	Total Price of Subcontract for Services or Supplies
		\$15,000.00
Power and control we	DEK	

Contractor / S Mechanical, Inc.	
Name Project Manage	
Title / /// // / / / / / / / / / / / / / /	1/24/2018
Prime Contractor Signature	Date

Cook County Office of the Chief Procurement Officer Identification of Subcontractor/Supplier/Subconsultant Form

	OCPO ONLY	
0	Disqualification	
0	Check Complete	

The Bidder/Proposer/Respondent ("the Contractor") will fully complete and execute and submit an identification of Subcontractor/Supplier/Subconsultant Form ("ISF") with each Bid, Request for Proposal, and Request for Qualification. The Contractor must complete the ISF for each Subcontractor, Supplier or Subconsulent which shall be used on the Contract. In the event that there are any changes in the utilization of Subcontractors, Suppliers or Subconsultants, the Contractor must file an updated ISF.

Bid/RFP/RFQ No:	1555-14	475-MC5	Date:	1/24/2018	
Total Bid or Propusal	Amount: \$354,61	8.16	Contract Title:	CCB Install Fluor	Drains-Penthouse &
Contractor:	S Mechanical, in	i¢.	Subcontractor/Supplier/ Subconsultant to be added or substitute	G&V Constructi	on Co. Inc.
Authorized Contact for Contractor	Dave Amacher		Authorized Contact for Subcontractor/Supplier/ Subconsultant	Anna Favuzzi	
Email Address (Contractor)	damacher@smi	echanical.com	Email Address (Subcontractor)	anna@gvconstr	uctionco.com
Company Address (Contractor)	16420 S Kilbourn		Company Address (Subcontractor)	5239 W Diverse	y Ave. Suite 201
City, State and Zip (Contractor)	Oak Forest, IL 6	0452	City, State and Zip (Subcontractor)	Chicago, IL 606	35
Telephone and Fax (Contractor)	708-535-3600 708-535-6655 F		Telephone and Fax (Subcontractor)	680-595-6474 630-595-6477	
Estimated Start and Completion Dates (Contractor)	Start: Completion:	3/5/2018 7/5/2018	Estimated Start and Completion Dates (Subcontractor)	Start: Completion:	3/5/2018 7/5/2018

Note: Upon request, a copy of all written subcontractor agreements must be provided to the OCPO.

Description of Services or Supplies	<u>Total Price of</u> <u>Subcontract for</u> Sarylces or Supplies
Concrete Work	\$80,782,00

Contractor		
of Mechanical, Inc.		
Varne /		
Project Manager		
itte //w ////////////////////////////////		
112 14 11/1/11/11/11	1/24/2018	
Prime Contractor Signature	Date	, ,,

Cook County Office of the Chief Procurement Officer Identification of Subcontractor/Supplier/Subconsultant Form

	OCPO ONLY	
0	Disqualification	
Ō	Check Complete	

The Bidder/Proposer/Respondent ("the Contractor") will fully complete and execute and submit an identification of Subcontractor/Supplier/Subconsultant Form ("ISF") with each Bid, Request for Proposal, and Request for Qualification. The Contractor must complete the ISF for each Subcontractor, Supplier or Subconsulant which shall be used on the Contract. In the event that there are any changes in the utilization of Subcontractors, Suppliers or Subconsultants, the Contractor must file an updated ISF.

Bid/RFP/RFQ Na:			Date:	1/24/2018	
Total Bid or Proposal	Amount: 35664	8.18	Contract Title:	CCB install Floor D & Equipment Roor	
Contractor:	5 Mechanical, Inc		Subcontractor/Supplier/ Subconsultant to be added or substitute	J.S.R. Enterprises, Inc.	
uthorized Contact Dave Amacher or Contractor		Authorized Contact for Subcontractor/Suppiler/ Subconsultant	Jerry Roberts		
Email Address (Contractor)	damacher@smechanical.com		Email Address (Subcontractor)	sroberts@isrent.com	
Company Address (Contractor)	16420 S Kilbourn		Company Address (Subcontractor)	4931 W 173rd St. Unit D	
City, State and Zip (Contractor)	Oak Forest, IL 60452		City, State and Zip (Subcontractor)	Country Club Hills, IL 60478	
Telephone and Fax (Contractor)	708-535-3600 708-535-6655 F		Telephone and Fax (Subcontractor)	708-206-1800 708-206-1879	
Estimated Start and Completion Dates (Contractor)	Start: Completion:	3/5/2018 7/5/2018	Estimated Start and Completion Dates (Subcontractor)	Start: Completion;	3/5/2018 7/5/2018

Note: Upon request, a copy of all written subcontractor agreements must be provided to the OCPO.

Description of Services or Supplies	Total Price of Subcontract for Services or Supplies
Plumbing Work	\$25,000.00

Contractor	
\$ Mechanical, Inc.	•
Name Project Manager	
Title Mee /////////////////////////////////	1/24/2018
Prime Contractor Signature	Date

SAM Search Results List of records matching your search for:

Search Term: jm polcurr* Record Status: Active

No Search Results

SAM Search Results List of records matching your search for:

Search Term: "g & v construction* Record Status: Active

ENTITY G & V Construction Inc

Status:Active

DUNS: 831658492

+4:

CAGE Code: 7UQE9

DoDAAC:

Expiration Date: Apr 11, 2018 Has Active Exclusion?: No

Debt Subject to Offset?: No

Address: 7823 W 145TH ST

City: SAVAGE

State/Province: MINNESOTA Country: UNITED STATES

ZIP Code: 55378-2887

SAM Search Results List of records matching your search for:

Search Term: j.s.r.* enterprises* Record Status: Active

No Search Results



PROCUREMENT SERVICES

We are the contracting authority for the procurement of goods and services for the City of Chicago

		-	MENU
Debarred Firms and Individuals			
IM POLCURR			
ENTITY/INDIVIDUAL	STREET ADDRESS	CITY	STATE
			·
		One was wear the same and was say that in the same	1000 AND 100
otals:		#	,
		Addition to come and representation of security and security Addition of	And the second s
ntities, individuals or both are sub ntities or individuals, date of deba ertains to individuals, permanent idividuals and entities that are ine 20 of the Municipal Code. Data is	rment, length of debarment of pertains to entities. In addition ligible to do business with the	and cause. Lifetir on, this list also ic	ne debarment lentifies
	parredFirms/DebarredList071	1.2 ndf)	



PROCUREMENT SERVICES

We are the contracting authority for the procurement of goods and services for the City of Chicago

			MENU
Debarred Firms and Individuals 3 & V CONSTRUCTION CO			
ENTITY/INDIVIDUAL	STREET ADDRESS	CITY	STATE
	• .		
			-
	•		
Totals:	and the state of t	gg menne van Milleljer. Van der vijl 49 kommen 1673 tot en derlikste van van de 184 meerste.	ر در
(Calif.		The second secon	nan Magair ann ann a' 19 Sainne an Aigh 19 a' r ann an daoi 18 Sainne an Annaidh 19 Sainn ann a Abhain
intities, individuals or both are su entities or individuals, date of deb pertains to individuals, permanen ndividuals and entities that are in 020 of the Municipal Code. Data is	parment, length of deparment of pertains to entities. In additionally neligible to do business with the	on, this list also ne City pursuant	identifies



PROCUREMENT SERVICES

We are the contracting authority for the procurement of goods and services for the City of Chicago

STREET ADDRESS	CITY	STATE
		•
	•	
when p_1 is p_2 in p_3 is p_4 in p_5 in the second constant of p_4 is p_5 in p_5 in p_6 in	Data and a language on the foreign foreign foreign for the foreign foreign foreign foreign foreign foreign foreign foreign for the foreign foreign foreign foreign foreign foreign foreign for the foreign foreign foreign foreign foreign foreign foreign for the foreign foreign foreign foreign foreign foreign foreign for the foreign for	AND AND AND AND AND AND THE STORY OF STORY OF THE STORY O
) (((()) (() (()) (()) (()) (()) (())	
rment, length of debarment a pertains to entities. In addition	nd cause. Lifetir n, this list also id	ne debarment lentifies
	rment, length of debarment a pertains to entities. In additior	ject to debarment. The following list provides rment, length of debarment and cause. Lifetin pertains to entities. In addition, this list also id ligible to do business with the City pursuant to
